

SRIVIN PLATFORMS

Delivery partner to RacingAhead / SportSeek

SportSeek — Unified Sports Ecosystem Platform

Work Breakdown Structure & Integrated Project Plan

Phase 2A — Harden & Unify, including the 20 October 2026 public launch

Document control	
Document	SRV-SPS-2A-PLN-001
Programme	SportSeek Phase 2 — Phase 2A (Harden & Unify)
Client	RacingAhead / SportSeek, Hyderabad
Prepared by	Srivin Platforms — Technical Programme Management Office
Version / date	v1.0 — 27 September 2026
Status	Issued for client review
Reference baseline	SportSeek Phase 2 SOW v1.0 (15 Jul 2026); SportsSeek App High Level Requirements
Classification	Confidential — RacingAhead / SportSeek and Srivin Platforms only

Contents

- 1. Purpose and how to use this plan
- 2. Executive summary
- 3. Feasibility of the 20 October 2026 target
- 4. Release strategy for Phase 2A
- 5. Planning basis and assumptions
- 6. Work Breakdown Structure (WBS) and WBS dictionary
- 7. Integrated schedule (Gantt)
- 8. Detailed activity schedule
- 9. Dependency management
- 10. Critical path and schedule risk
- 11. Milestones, gates and acceptance evidence
- 12. Sprint calendar
- 13. Resource plan, loading and technical skills
- 14. Baseline control and re-planning rules
- Appendix A. SOW-to-WBS traceability

1. Purpose and how to use this plan

This document is the integrated project plan for Phase 2A of the SportSeek programme, prepared by Srivin Platforms as delivery partner to RacingAhead / SportSeek. It breaks the Phase 2A scope defined in the SportSeek Phase 2 Statement of Work (SOW) into a Work Breakdown Structure (WBS), schedules every work package, and makes each dependency, whether internal or on SportSeek and third parties, explicit and dated.

The plan is built only from what the two source documents state. Where the SOW flags an item as open (marked  in the SOW), this plan does not assume an answer. It records the item as a dated decision that SportSeek needs to make (Section 9.3), along with what happens to the schedule if the decision is late.

1.1 Companion documents

Document	Purpose
SRV-SPS-2A-PLN-001 (this document)	WBS, schedule, dependencies, critical path, milestones, resource loading and skills
SRV-SPS-2A-DLM-002 Project Delivery Model	How we deliver: lifecycle, agile cadence, governance, quality, release, change, risk, KT and support
SRV-SPS-2A-TAD-003 Technical Approach	How we solve the problem technically: architecture, per-module design approach, engineering practices
SRV-SPS-2A-PLN-001a Project Plan workbook (.xlsx)	The same schedule, dependency register and resource loading in spreadsheet form, for import into SportSeek's chosen tool (JIRA or Trello)

1.2 Conventions

- **Dates** are calendar dates in IST. Durations are in working days (Monday–Friday). Indian public and festival holidays will be applied once the joint holiday calendar is agreed at kick-off (see Assumption A6).
- **Owner**: "Srivin" = Srivin Platforms; "SportSeek" = RacingAhead / SportSeek; "Joint" = both parties, with Srivin driving.
- **Predecessors** use WBS IDs. A bare ID means Finish-to-Start (FS). "SS" means Start-to-Start. IDs starting with "D" are external dependencies from the register in Section 9.3.
- **Milestone numbers M1–M6** keep the SOW Section 12.1 numbering so both parties can trace them.

2. Executive summary

Phase 2A turns SportSeek's live Phase 1 product (User App, Partner App and Admin Web Portal) into a unified platform. It adds one shared identity, one transaction view, one generalised partner/service model, a multi-channel notification platform, hardened booking/event flows and a full web application. The SOW's own indicative estimates put this at 26–37 weeks of work if done in sequence, before knowledge transfer.

SportSeek wants to be available to the public on **20 October 2026**. We have planned for that date directly and honestly: **SportSeek goes public on 20 October 2026 with a hardened, security-tested and monitored Phase 1 product (Release 2A.0)**. The remaining Phase 2A scope follows in three planned releases, each with its own UAT, go-live and knowledge transfer. That gives the public a stable product on the target date and does not risk an unstable launch of half-built features.

Release	What goes live	Go-live
2A.0 Public Launch	Phase 1 User App, Partner App and Admin Portal, hardened for public traffic: critical/high defects closed, security-tested, load-tested, monitored, store- and DPDP-ready. Plus gate-approved quick wins only.	Tue 20 Oct 2026
2A.1 Unify	M2 Shared Identity (account linking, roles, KYC reuse, migration of existing accounts) + M6 Notification core (Push, Email, templates, role-scoped preferences)	Wed 27 Jan 2027
2A.2 Generalise & Harden	M5 Generalised Partner & Service model (coach, physio, nutritionist) + M4 Booking/Events hardening (cancellation, refunds, waitlist, edit notifications) + WhatsApp + full alert catalog	Tue 16 Mar 2027
2A.3 Transact & Web	M3 Transaction Ledger + full Web Application + data import tools. Phase 2A complete.	Tue 4 May 2027

Key messages for the steering committee

1. 20 October 2026 is achievable for a hardened public launch. It depends on seven SportSeek inputs arriving between 29 September and 9 October (D1–D7). The most time-critical are code and infrastructure access on 29 September and launch scope sign-off on 1 October.
2. Full Phase 2A completes on 4 May 2027, with the final hypercare and KT sign-off by 4 June 2027. That is roughly 31 weeks from kick-off, inside the SOW's 26–37 week sequential estimate, because we run five build streams in parallel.
3. The critical path runs through design-system approval (20 Nov 2026) and the web application build into the final release. A second, near-critical chain (Shared Identity → Partner/Service generalisation with Razorpay Route onboarding → Transaction Ledger) has only about two weeks of float. Written confirmation that Razorpay Route is enabled for the new partner categories (D10, needed by 6 Nov 2026) is the single most important external dependency.
4. Phase 2A design and discovery start on 5 October, alongside the launch. Building for 2A therefore begins on 16 November without waiting for launch hypercare to end.

3. Feasibility of the 20 October 2026 target

As at the date of this plan (Sunday 27 September 2026) there are 16 working days before 20 October 2026. The SOW itself gives indicative durations for the Phase 2A milestones:

SOW milestone	Scope (SOW 12.1)	SOW indicative duration
M1 — Foundation Setup	Environment/CI-CD within SportSeek infra, security baseline	2–3 weeks
M2 — Shared Identity	Unified identity, account linking, role management	6–8 weeks
M3 — Transaction Ledger	Ledger views on top of existing gateway	4–6 weeks
M4 — Booking/Events Hardening	Cancellation, waitlists, edit-notifications	4–6 weeks
M5 — Generalised Partner/Service	Facility model generalised; coach/physio/nutritionist types	6–8 weeks
M6 — Notification Expansion	Push, WhatsApp, Email; alert catalog	4–6 weeks
Total if sequential	Excludes KT (2 weeks–1 month per milestone, SOW 12.2), UAT, and design	26–37 weeks
Web application (SOW 3.1)	Port of all Phase 1 mobile functionality to a full web application	Not estimated in SOW

The SOW also requires, before go-live, UI/UX approved before development (SOW 14.2), a penetration test (SOW 6.2), load testing (SOW 6.2), UAT by SportSeek testers (SOW 5), and HLD/LLD per module (SOW 13). **No reading of these requirements allows the new Phase 2A modules to be built, tested and accepted in 16 working days.** Promising otherwise would put SportSeek's public reputation and live payment flows at risk.

3.1 What the public launch on 20 October 2026 includes

In Release 2A.0 (20 Oct 2026)	Delivered later (release)
All live Phase 1 journeys (SOW 2.1): registration, venue search by name/sport/radius, availability and slots, create/publish/edit events, tournaments, multi-tournament registration with payment, partner facility onboarding and verification, admin oversight	Shared identity and account linking (2A.1)
Critical and high-severity Phase 1 defects in launch scope closed	Push and Email channels, template management (2A.1)
Security baseline: SAST, dependency and DAST scans; VAPT of the launch surface with no open critical/high findings	Coach/physio/nutritionist partner types (2A.2)
Load test at SportSeek-defined launch concurrency	Cancellation and refund flows, waitlist (2A.2)
Production monitoring, alerting, error tracking; launch runbook and rollback plan	WhatsApp and the full alert catalog (2A.2)
Store and privacy readiness: store listings, privacy policy, DPDP notice/consent, in-app account deletion check	Transaction Ledger (2A.3)
Only quick wins approved at the 1 Oct Scope Gate that fit the 14 Oct code freeze	Full web application (2A.3)
Hypercare 20 Oct – 13 Nov 2026 and ongoing Phase 1 support (SOW 16)	Offline data import tools (2A.3)

Launch-date conditions (non-negotiable for a safe launch)

The 20 Oct date holds only if: **(a)** the NDA/SOW is executed and access to code, infrastructure, store consoles and the gateway dashboard is granted by **29 Sep**; **(b)** the launch scope is frozen at the Scope Gate on **1 Oct**; **(c)** legal content (privacy policy, terms, DPDP notice) is supplied by **9 Oct**; **(d)** SportSeek UAT testers are available **15–19 Oct**.

If the Phase 1 assessment (2.1) finds a defect or vulnerability that cannot be closed by the 14 Oct freeze, Srivin will raise it the same day with options (fix and slip, mitigate, or de-scope the affected journey). The Go/No-Go decision on 19 Oct remains SportSeek's.

4. Release strategy for Phase 2A

The SOW asks for Phase 2A to "start with hardening and unifying what already exists in production" and to be delivered "as milestones within each phase", not "all-at-once" (SOW 1, 3). We group the six SOW milestones into four releases. The grouping follows the technical dependency order: identity first, because every other module depends on it (SOW 6.1).

Release	SOW milestones	Rationale for grouping	Build window	Go-live
2A.0	M1 (launch subset), Phase 1 support	Make the live product safe for public traffic; no new domain changes during launch	28 Sep – 14 Oct 2026	20 Oct 2026
2A.1	M1 (rest), M2, M6 core	Identity is the foundation for roles, ledger, partner types and role-scoped notifications. Notification core is needed by M4 edit/waitlist alerts.	16 Nov 2026 – 8 Jan 2027	27 Jan 2027
2A.2	M5, M4, M6 complete	The partner model and booking data model must be designed together (SOW 9.3 "consistent data model"). Waitlist and edit triggers use the full catalog.	28 Dec 2026 – 5 Mar 2027	16 Mar 2027
2A.3	M3, Web app, import tools	The Ledger needs identity, Route-onboarded partners and refund flows first. The web app reaches parity once all 2A features exist.	30 Nov 2026 – 2 Apr 2027	4 May 2027

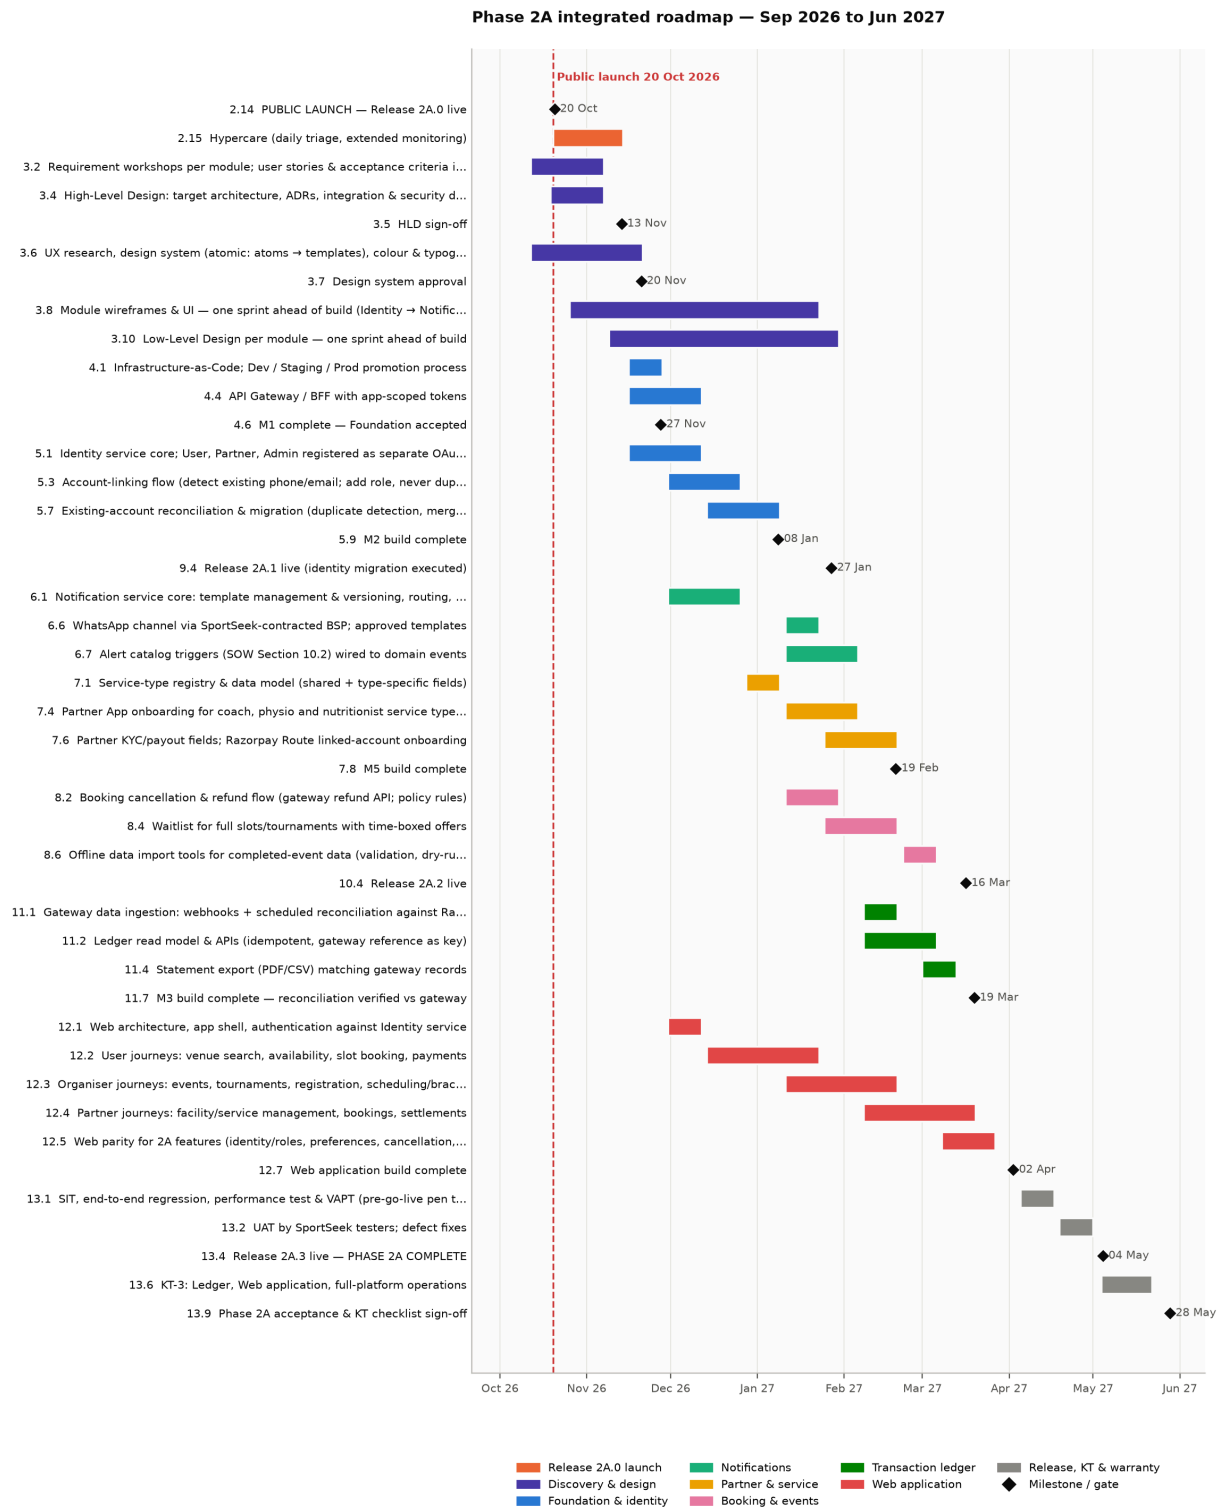


Figure 1 — Phase 2A integrated roadmap (summary level; all activities are listed in Section 8)

5. Planning basis and assumptions

#	Assumption	If it does not hold
A1	Kick-off on Tue 29 Sep 2026, with NDA and SOW/PO executed by then (SOW 19, Next Steps).	Launch date is at risk day-for-day
A2	SportSeek provides Phase 1 source code, DB schema and API documentation before kick-off (SOW 5).	Assessment and launch hardening slip
A3	All cloud, repository, store and third-party accounts are SportSeek-owned; Srivin works within them (SOW 5, 15).	Access requests on the critical path
A4	A named SportSeek Product Owner is available for decisions (SOW 5). During the launch window, a decision within 1 working day.	Decisions escalate via governance (Delivery Model §6)
A5	SportSeek supplies dedicated UAT testers within the UAT windows in this plan (SOW 5).	Go-live dates move with UAT
A6	Plan uses a Mon–Fri calendar. The joint holiday calendar (national and festival holidays in the Oct–Jan period) is agreed at kick-off, and capacity rather than dates is adjusted first.	Sprint capacity re-planned
A7	SportSeek developers join the Srivin squads from Sprint 1 (SOW 5). Their capacity is additional to the Srivin core team in Section 13.	Plan remains valid; KT effort increases
A8	The existing payment gateway is Razorpay and SMS provider contracts remain in place (SOW 5, 8.3). Route split settlement will be integrated (SOW 8.3 NOTE).	Ledger design re-opened via change request
A9	Transaction Ledger scope is the Admin dashboard plus a partner settlement view in the web application, as in SOW 8.1–8.2. Any User/Partner mobile app ledger view (SOW 8.1 open item; SOW 12.1 M3 wording) is confirmed by D15.	Adds about 1 sprint to M3 via change request
A10	Phase 2B and 2C scope (Community, Expert Booking UX, Analytics, Academy, Marketplace, Rewards) is excluded from this plan (SOW 3.2–3.3), except that domain events are designed in 2A so 2B analytics can consume them.	—
A11	The 2A.0 launch excludes new Phase 2A domain features. Anything added at the Scope Gate must fit within the 14 Oct code freeze.	Launch risk rises; Go/No-Go may fail
A12	Two-week sprints from 16 Nov 2026. LLD and UI for each module are produced one sprint ahead of build.	—
A13	Technology stack as confirmed by SportSeek: React Native mobile apps, .NET back end, PostgreSQL database. Phase 2A extends this stack; the new web application uses React (TypeScript) to share skills and design tokens with the React Native apps (Section 13.1).	Skills mix in Section 13 re-planned

6. Work Breakdown Structure (WBS) and WBS dictionary

The WBS is deliverable-oriented and follows the 100% rule: every Phase 2A scope item in SOW Section 3.1, and every deliverable in SOW Section 13, maps to exactly one work package (see Appendix A). Level 1 elements are shown below; Level 2 work packages, their deliverables and completion criteria follow in the dictionary.

6.1 WBS hierarchy (Levels 1–2)

L1	Element	Level-2 work packages
1	Programme Management & Governance	1.1 Mobilisation · 1.2 Kick-off · 1.3 Integrated plan & RAID · 1.4 Governance cadence · 1.5 Change control · 1.6 Re-baseline · 1.7 Closure
2	Release 2A.0 — Public Launch	2.1 Assessment · 2.2 Scope Gate · 2.3 Env/CI-CD/observability · 2.4 Defect remediation · 2.5 Security baseline & VAPT · 2.6 Load test · 2.7 Store & DPDP readiness · 2.8 Quick wins · 2.9 Code freeze · 2.10 Store submission · 2.11 Regression & UAT · 2.12 Runbook · 2.13 Go/No-Go · 2.14 Launch · 2.15 Hypercare · 2.16 KT-0
3	Discovery, Architecture & Design	3.1 Phase 1 deep-dive · 3.2 Requirements & stories · 3.3 Open-item closure · 3.4 HLD · 3.5 HLD sign-off · 3.6 Design system · 3.7 Design approval · 3.8 Module UI · 3.9 Web UX · 3.10 LLD · 3.11 Test strategy
4	Platform Foundation (M1)	4.1 IaC & environments · 4.2 CI/CD quality gates · 4.3 Event bus · 4.4 API Gateway/BFF · 4.5 Observability · 4.6 M1 acceptance
5	M2 Shared Identity	5.1 Identity core (OIDC) · 5.2 Registration/OTP/login · 5.3 Account linking · 5.4 Roles · 5.5 KYC reuse · 5.6 Profile & credentials · 5.7 Account reconciliation & migration · 5.8 Backward compatibility · 5.9 Build complete
6	M6 Notification Platform	6.1 Notification core · 6.2 Push · 6.3 Email · 6.4 Preferences & deep links · 6.5 Core complete · 6.6 WhatsApp · 6.7 Alert catalog triggers
7	M5 Partner & Service Model	7.1 Service-type registry · 7.2 Facility migration · 7.3 Admin type config · 7.4 Partner onboarding (new types) · 7.5 Verification workflow · 7.6 KYC & Route onboarding · 7.7 User App visibility · 7.8 Build complete
8	M4 Booking/Events Hardening	8.1 Unified data model · 8.2 Booking cancel/refund · 8.3 Tournament cancel/refund · 8.4 Waitlist · 8.5 Edit notifications · 8.6 Import tools · 8.7 Build complete
9	Release 2A.1	9.1 SIT · 9.2 UAT · 9.3 Go/No-Go · 9.4 Go-live · 9.5 KT-1 · 9.6 Warranty
10	Release 2A.2	10.1 SIT/perf/VAPT · 10.2 UAT · 10.3 Go/No-Go · 10.4 Go-live · 10.5 KT-2 · 10.6 Warranty
11	M3 Transaction Ledger	11.1 Gateway ingestion & reconciliation · 11.2 Read model & APIs · 11.3 Admin ledger screens · 11.4 Statement export · 11.5 Refund tracker · 11.6 Partner settlement view · 11.7 Build complete
12	Web Application	12.1 Shell & auth · 12.2 User journeys · 12.3 Organiser journeys · 12.4 Partner journeys · 12.5 2A parity · 12.6 Browser/a11y/SEO testing · 12.7 Build complete
13	Release 2A.3 & Phase Closure	13.1 SIT/perf/pen test · 13.2 UAT · 13.3 Go/No-Go · 13.4 Go-live · 13.5 Hypercare · 13.6 KT-3 · 13.7 Ops runbook & transition plan · 13.8 Warranty · 13.9 Phase acceptance
14	Continuous Support	14.1 Phase 1 production monitoring & bug fixes · 14.2 Launch warranty

6.2 WBS dictionary — key work packages

WBS	Work package	Key deliverables	Completion / acceptance criteria	SOW ref.
2.1	Phase 1 assessment	Assessment report: architecture, code quality, security findings, defect backlog triage, infra/backup posture, launch risks	Report reviewed at the Scope Gate; every launch risk has an owner and a decision	5, 16
2.5	Security baseline	Scan reports (SAST, dependency, DAST); VAPT report for launch surface; remediation log	No open critical/high findings at Go/No-Go	6.2, 14.1
2.6	Load test	Load-test scripts and report against the D5 concurrency figure; capacity recommendations	Agreed launch concurrency sustained within agreed error and latency thresholds	6.2
2.12	Launch runbook	Runbook, rollback plan, on-call rota, war-room protocol, communication templates	Walkthrough completed with SportSeek; rollback rehearsed on Staging	15

WBS	Work package	Key deliverables	Completion / acceptance criteria	SOW ref.
3.4	High-Level Design	Target architecture, ADRs, integration design (Razorpay incl. Route, SMS, Push, WhatsApp, Email), security and data-privacy design, NFR targets	HLD signed off by SportSeek (3.5)	6, 13
3.6	Design system	Atomic component library (atoms → templates), colour and typography system, UX principles	Approved by SportSeek before development (3.7)	13, 14.2
3.10	LLD per module	API contracts (OpenAPI), DB changes and ER diagrams, sequence diagrams, test cases linked to stories	Reviewed by Srivin architect and SportSeek tech reviewer before sprint start	9, 13
5.3	Account linking	Linking flow for phone/email match; ownership proof by OTP; role addition; user messaging per SOW 7.3	Partner App registration with an existing User App phone/email links to the same identity, with no duplicate created	7.3, 9.1
5.7	Account reconciliation	Duplicate-identity detection report on existing Phase 1 data; merge rules; migration scripts; rollback	SportSeek approves merge rules (D18); migration dry-run reconciles 100% of records	7.3, 17
6.1	Notification core	Notification service, template store with versioning, routing rules, delivery tracking, retry/fallback	All live SMS triggers (SOW 10.1) run through the new service unchanged	10
7.1–7.3	Service-type model	Shared + type-specific service schema; admin configuration; facility migration	A new service type can be enabled from the admin dashboard with no code change; existing facility partners unaffected	9.4
7.6	Route onboarding	Partner KYC/payout fields passed to Razorpay; linked-account creation	Test partners of every type onboard and receive split settlement in the Razorpay test environment	8.3
8.2–8.4	Booking hardening	Cancellation and refund via gateway refund API; policy rules; waitlist with timed offers	All Phase 1 flows unchanged (regression green); new flows pass SOW 9.3 acceptance	9.3
11.1–11.7	Transaction Ledger	Ingestion and reconciliation, ledger APIs, admin screens, exports, refund tracker, partner settlement view	Every gateway transaction appears within the agreed sync window; exports match gateway records exactly	8.2
12.x	Web application	Responsive web app for User, Organiser and Partner journeys	Feature-parity checklist vs mobile signed off; cross-browser and accessibility checks pass	3.1
13.7	Ops runbook & transition	Infrastructure operations runbook; transition plan for SportSeek in-house team	SportSeek ops team completes runbook walkthrough; transition timeline agreed	13, 15.1
2.16, 9.5, 10.5, 13.6	Knowledge transfer	KT sessions, recordings, KT checklist per milestone	KT checklist signed by SportSeek and Srivin	12.2

7. Integrated schedule (Gantt)

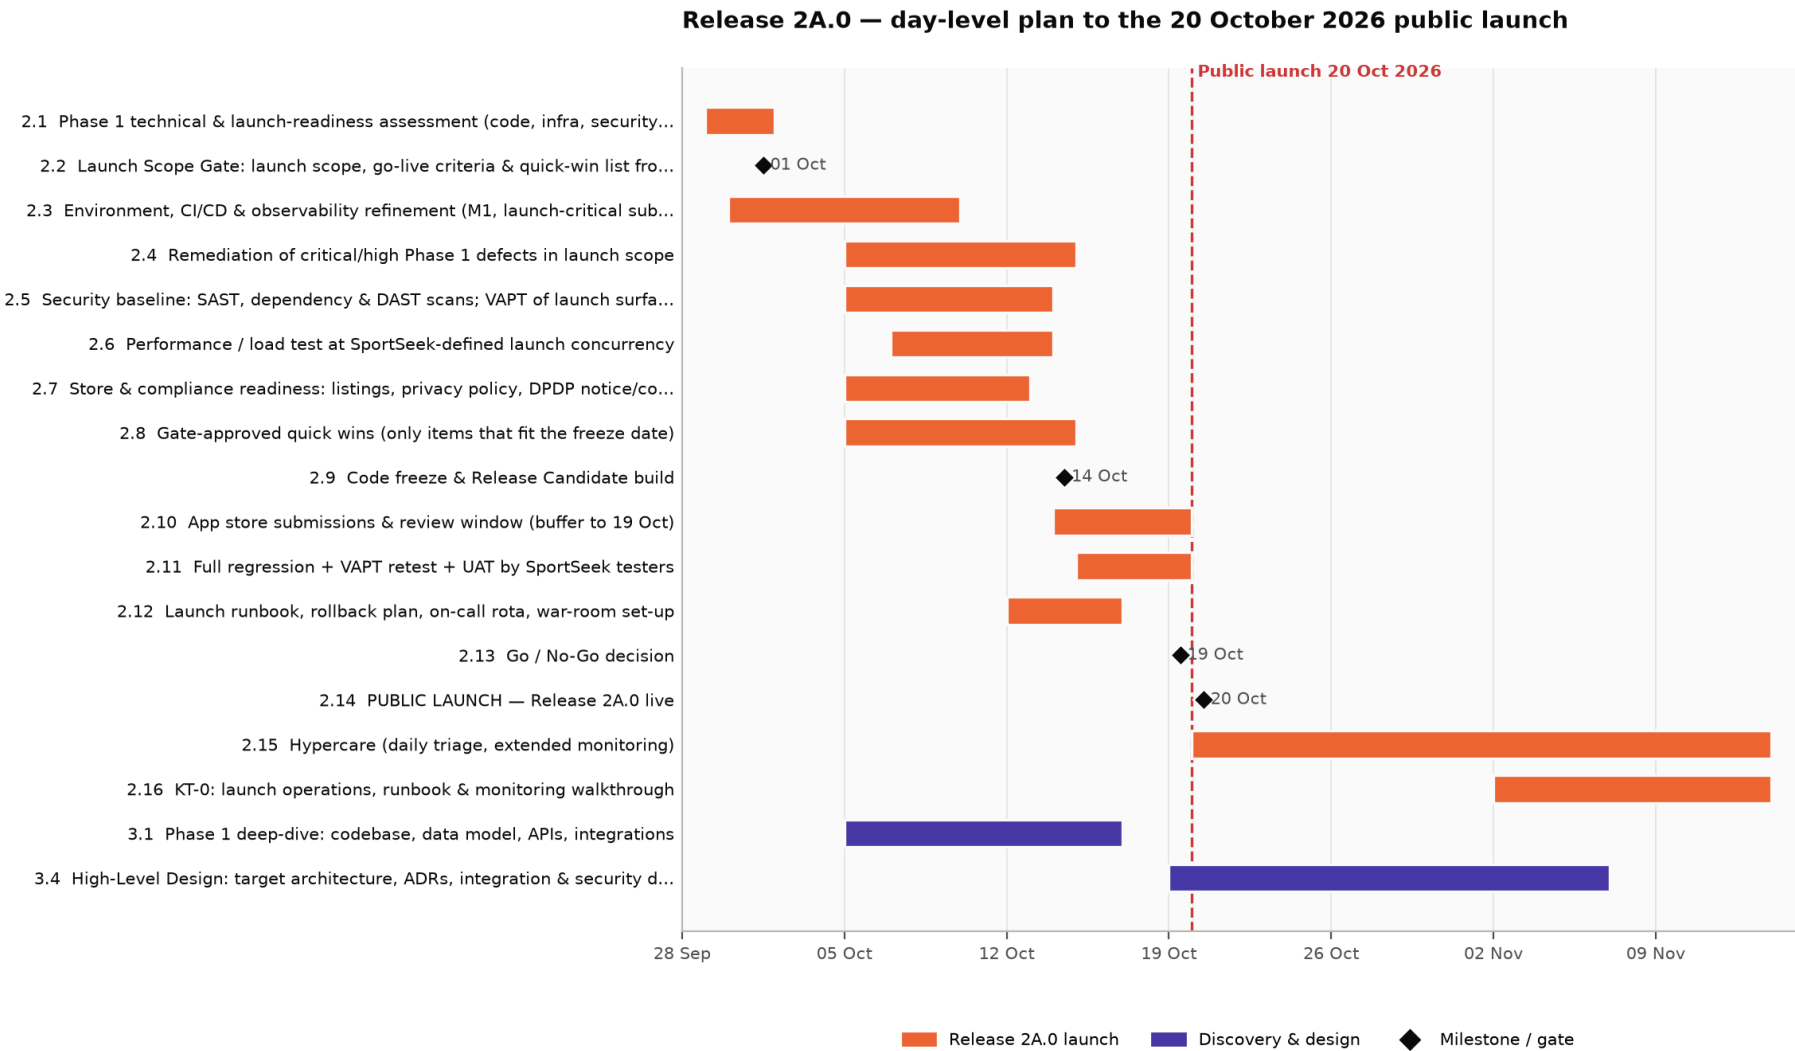


Figure 2 — Release 2A.0: day-level plan to the 20 October 2026 public launch

8. Detailed activity schedule

The full activity list with owners, dates, working-day durations and predecessors. The same data is in the accompanying workbook (SRV-SPS-2A-PLN-001a) for import into SportSeek's chosen tool.

WBS	Activity	Owner	Start	Finish	Days	Predecessors
1 Programme Management & Governance (28 Sept 26 – 04 Jun 27)						
1.1	Mobilisation: NDA, SOW/PO execution, team onboarding, access provisioning	Joint	28 Sept 26	30 Sept 26	3	—
1.2	◆ Kick-off workshop (SportSeek + Srivin)	Joint	29 Sept 26	29 Sept 26	0	1.1SS
1.3	Integrated plan, RAID log, communication plan, governance charter	Srivin	29 Sept 26	09 Oct 26	9	1.2
1.4	Governance cadence: daily stand-ups, weekly status, fortnightly demos, monthly steering	Srivin	30 Sept 26	04 Jun 27	178	1.2
1.5	Change control (per SOW Section 18) — ongoing	Joint	30 Sept 26	04 Jun 27	178	1.2
1.6	◆ Phase 2A plan re-baseline & milestone costing sign-off	SportSeek	13 Nov 26	13 Nov 26	0	3.4FS, 3.3FS
1.7	Phase 2A closure: completion report, lessons learned, handover sign-off	Joint	31 May 27	04 Jun 27	5	13.9
2 Release 2A.0 — Public Launch (20 Oct 2026) (29 Sept 26 – 13 Nov 26)						
2.1	Phase 1 technical & launch-readiness assessment (code, infra, security, data, defects)	Srivin	29 Sept 26	01 Oct 26	3	1.2
2.2	◆ Launch Scope Gate: launch scope, go-live criteria & quick-win list frozen	SportSeek	01 Oct 26	01 Oct 26	0	2.1
2.3	Environment, CI/CD & observability refinement (M1, launch-critical subset)	Srivin	30 Sept 26	09 Oct 26	8	1.2
2.4	Remediation of critical/high Phase 1 defects in launch scope	Joint	05 Oct 26	14 Oct 26	8	2.2
2.5	Security baseline: SAST, dependency & DAST scans; VAPT of launch surface	Srivin	05 Oct 26	13 Oct 26	7	2.2
2.6	Performance / load test at SportSeek-defined launch concurrency	Srivin	07 Oct 26	13 Oct 26	5	2.3SS, D5
2.7	Store & compliance readiness: listings, privacy policy, DPDP notice/consent, account deletion check	Joint	05 Oct 26	12 Oct 26	6	2.2, D6
2.8	Gate-approved quick wins (only items that fit the freeze date)	Joint	05 Oct 26	14 Oct 26	8	2.2
2.9	◆ Code freeze & Release Candidate build	Srivin	14 Oct 26	14 Oct 26	0	2.4, 2.8
2.10	App store submissions & review window (buffer to 19 Oct)	Joint	14 Oct 26	19 Oct 26	4	2.9, 2.7
2.11	Full regression + VAPT retest + UAT by SportSeek testers	Joint	15 Oct 26	19 Oct 26	3	2.9
2.12	Launch runbook, rollback plan, on-call rota, war-room set-up	Srivin	12 Oct 26	16 Oct 26	5	2.3
2.13	◆ Go / No-Go decision	SportSeek	19 Oct 26	19 Oct 26	0	2.10, 2.11, 2.12
2.14	◆ PUBLIC LAUNCH — Release 2A.0 live	Joint	20 Oct 26	20 Oct 26	0	2.13
2.15	Hypercare (daily triage, extended monitoring)	Srivin	20 Oct 26	13 Nov 26	19	2.14

WBS	Activity	Owner	Start	Finish	Days	Predecessors
2.16	KT-0: launch operations, runbook & monitoring walkthrough	Srvin	02 Nov 26	13 Nov 26	10	2.14
3 Phase 2A Discovery, Architecture & Design (05 Oct 26 – 29 Jan 27)						
3.1	Phase 1 deep-dive: codebase, data model, APIs, integrations	Srvin	05 Oct 26	16 Oct 26	10	1.1, D2
3.2	Requirement workshops per module; user stories & acceptance criteria in SportSeek tool	Joint	12 Oct 26	06 Nov 26	20	3.1SS, D8
3.3	Closure of open items flagged in SOW (ledger visibility, alert catalog, SLAs, perf targets, refund policy, Route enablement)	SportSeek	05 Oct 26	06 Nov 26	25	D10, D11, D15, D16, D20
3.4	High-Level Design: target architecture, ADRs, integration & security design	Srvin	19 Oct 26	06 Nov 26	15	3.1
3.5	◆ HLD sign-off	SportSeek	13 Nov 26	13 Nov 26	0	3.4
3.6	UX research, design system (atomic: atoms → templates), colour & typography	Srvin	12 Oct 26	20 Nov 26	30	3.2SS
3.7	◆ Design system approval	SportSeek	20 Nov 26	20 Nov 26	0	3.6
3.8	Module wireframes & UI — one sprint ahead of build (Identity → Notifications → Partner → Booking → Ledger)	Srvin	26 Oct 26	22 Jan 27	65	3.6SS
3.9	Web application UX (responsive layouts for all Phase 1 journeys)	Srvin	16 Nov 26	29 Jan 27	55	3.6SS
3.10	Low-Level Design per module — one sprint ahead of build	Srvin	09 Nov 26	29 Jan 27	60	3.4
3.11	Test strategy & automation approach sign-off	Srvin	02 Nov 26	13 Nov 26	10	3.4SS
4 Platform Foundation (M1 — refine) (16 Nov 26 – 11 Dec 26)						
4.1	Infrastructure-as-Code; Dev / Staging / Prod promotion process	Srvin	16 Nov 26	27 Nov 26	10	3.5
4.2	CI/CD quality gates: tests, coverage, SAST, dependency & secret scanning	Srvin	16 Nov 26	27 Nov 26	10	3.5
4.3	Async event bus foundation (transactional outbox)	Srvin	16 Nov 26	27 Nov 26	10	3.5
4.4	API Gateway / BFF with app-scoped tokens	Srvin	16 Nov 26	11 Dec 26	20	3.5
4.5	Observability: tracing, dashboards, alerting	Srvin	16 Nov 26	27 Nov 26	10	2.3
4.6	◆ M1 complete — Foundation accepted	SportSeek	27 Nov 26	27 Nov 26	0	4.1, 4.2, 4.3, 4.5
5 M2 — Shared Identity (16 Nov 26 – 08 Jan 27)						
5.1	Identity service core; User, Partner, Admin registered as separate OAuth2/OIDC clients	Srvin	16 Nov 26	11 Dec 26	20	3.5
5.2	Registration, OTP & login refactor on User, Partner and Admin clients	Joint	16 Nov 26	25 Dec 26	30	5.1SS
5.3	Account-linking flow (detect existing phone/email; add role, never duplicate)	Srvin	30 Nov 26	25 Dec 26	20	5.1SS
5.4	Role management (multi-role identity; role-scoped data)	Srvin	30 Nov 26	25 Dec 26	20	5.1SS
5.5	KYC/verification attached to identity and reused across roles	Srvin	14 Dec 26	25 Dec 26	10	5.4SS
5.6	Profile management; credential changes applied to the one shared account	Srvin	14 Dec 26	25 Dec 26	10	5.1
5.7	Existing-account reconciliation & migration (duplicate detection, merge rules)	Joint	14 Dec 26	08 Jan 27	20	5.3SS, D18

WBS	Activity	Owner	Start	Finish	Days	Predecessors
5.8	Backward compatibility for live app versions; forced-upgrade strategy	Srvin	28 Dec 26	08 Jan 27	10	5.2
5.9	◆ M2 build complete	Srvin	08 Jan 27	08 Jan 27	0	5.2, 5.3, 5.4, 5.5, 5.6, 5.7, 5.8
6 M6 — Notification Platform Expansion (30 Nov 26 – 05 Feb 27)						
6.1	Notification service core: template management & versioning, routing, delivery tracking	Srvin	30 Nov 26	25 Dec 26	20	4.3, D12
6.2	Push channel (FCM / APNs)	Srvin	14 Dec 26	25 Dec 26	10	6.1SS, D14
6.3	Email channel (SportSeek-contracted provider)	Srvin	14 Dec 26	25 Dec 26	10	6.1SS, D14
6.4	Role-scoped notification preferences; cross-app deep links with app-switch handling	Srvin	28 Dec 26	08 Jan 27	10	6.1, 5.4
6.5	◆ Notification core build complete (ships in 2A.1)	Srvin	08 Jan 27	08 Jan 27	0	6.1, 6.2, 6.3, 6.4
6.6	WhatsApp channel via SportSeek-contracted BSP; approved templates	Srvin	11 Jan 27	22 Jan 27	10	6.5, D13
6.7	Alert catalog triggers (SOW Section 10.2) wired to domain events	Srvin	11 Jan 27	05 Feb 27	20	6.5, D12
7 M5 — Generalised Partner & Service Model (28 Dec 26 – 19 Feb 27)						
7.1	Service-type registry & data model (shared + type-specific fields)	Srvin	28 Dec 26	08 Jan 27	10	3.10SS, 5.4
7.2	Migration of existing facilities to the generalised model (zero regression)	Srvin	04 Jan 27	22 Jan 27	15	7.1SS
7.3	Admin configuration to enable new service types without code	Srvin	11 Jan 27	22 Jan 27	10	7.1
7.4	Partner App onboarding for coach, physio and nutritionist service types	Joint	11 Jan 27	05 Feb 27	20	7.1, 5.9
7.5	Verification workflow per service type (Admin Portal)	Srvin	25 Jan 27	05 Feb 27	10	7.3
7.6	Partner KYC/payout fields; Razorpay Route linked-account onboarding	Srvin	25 Jan 27	19 Feb 27	20	7.4SS, D10
7.7	Verified services visible in User App listings	Srvin	08 Feb 27	19 Feb 27	10	7.5
7.8	◆ M5 build complete	Srvin	19 Feb 27	19 Feb 27	0	7.2, 7.4, 7.5, 7.6, 7.7
8 M4 — Booking, Events & Tournaments Hardening (11 Jan 27 – 05 Mar 27)						
8.1	Consistent event/tournament data model aligned with Partner/Service model	Srvin	11 Jan 27	15 Jan 27	5	7.1
8.2	Booking cancellation & refund flow (gateway refund API; policy rules)	Srvin	11 Jan 27	29 Jan 27	15	8.1SS, D11
8.3	Tournament registration cancellation & refund	Srvin	25 Jan 27	05 Feb 27	10	8.2SS
8.4	Waitlist for full slots/tournaments with time-boxed offers	Srvin	25 Jan 27	19 Feb 27	20	8.1, 6.5
8.5	Event-edited-after-publish notifications to registered users	Srvin	08 Feb 27	19 Feb 27	10	6.7
8.6	Offline data import tools for completed-event data (validation, dry-run)	Srvin	22 Feb 27	05 Mar 27	10	8.1, D19
8.7	◆ M4 build complete	Srvin	19 Feb 27	19 Feb 27	0	8.2, 8.3, 8.4, 8.5
9 Release 2A.1 — Shared Identity + Notification Core (11 Jan 27 – 27 Apr 27)						
9.1	System integration test, regression & security scan	Srvin	11 Jan 27	15 Jan 27	5	5.9, 6.5

WBS	Activity	Owner	Start	Finish	Days	Predecessors
9.2	UAT by SportSeek testers; defect fixes	Joint	18 Jan 27	22 Jan 27	5	9.1
9.3	◆ Go / No-Go 2A.1	SportSeek	25 Jan 27	25 Jan 27	0	9.2
9.4	◆ Release 2A.1 live (identity migration executed)	Joint	27 Jan 27	27 Jan 27	0	9.3
9.5	KT-1: Identity & Notification (checklist sign-off)	Srvin	27 Jan 27	09 Feb 27	10	9.4
9.6	90-day warranty — 2A.1	Srvin	27 Jan 27	27 Apr 27	65	9.4
10 Release 2A.2 — Partner Generalisation + Booking Hardening + Multi-channel (22 Feb 27 – 14 Jun 27)						
10.1	SIT, regression, performance test & VAPT	Srvin	22 Feb 27	05 Mar 27	10	7.8, 8.7, 6.7
10.2	UAT by SportSeek testers; defect fixes	Joint	08 Mar 27	12 Mar 27	5	10.1
10.3	◆ Go / No-Go 2A.2	SportSeek	15 Mar 27	15 Mar 27	0	10.2
10.4	◆ Release 2A.2 live	Joint	16 Mar 27	16 Mar 27	0	10.3
10.5	KT-2: Partner/Service, Booking hardening, Notifications	Srvin	16 Mar 27	30 Mar 27	11	10.4
10.6	90-day warranty — 2A.2	Srvin	16 Mar 27	14 Jun 27	65	10.4
11 M3 — Transaction Ledger (08 Feb 27 – 19 Mar 27)						
11.1	Gateway data ingestion: webhooks + scheduled reconciliation against Razorpay APIs	Srvin	08 Feb 27	19 Feb 27	10	5.9, D10
11.2	Ledger read model & APIs (idempotent, gateway reference as key)	Srvin	08 Feb 27	05 Mar 27	20	11.1SS
11.3	Admin ledger: history (filters, sort on every column), transaction detail	Srvin	22 Feb 27	05 Mar 27	10	11.2SS, 3.8
11.4	Statement export (PDF/CSV) matching gateway records	Srvin	01 Mar 27	12 Mar 27	10	11.2SS
11.5	Refund status tracker	Srvin	08 Mar 27	19 Mar 27	10	8.2, 11.2
11.6	Partner settlement view (web application)	Srvin	08 Mar 27	19 Mar 27	10	7.6, 11.2, 12.1
11.7	◆ M3 build complete — reconciliation verified vs gateway	Srvin	19 Mar 27	19 Mar 27	0	11.3, 11.4, 11.5, 11.6
12 Web Application (port of Phase 1 mobile functionality) (30 Nov 26 – 02 Apr 27)						
12.1	Web architecture, app shell, authentication against Identity service	Srvin	30 Nov 26	11 Dec 26	10	3.7, 4.4SS
12.2	User journeys: venue search, availability, slot booking, payments	Srvin	14 Dec 26	22 Jan 27	30	3.9SS, 12.1
12.3	Organiser journeys: events, tournaments, registration, scheduling/brackets, scoring	Srvin	11 Jan 27	19 Feb 27	30	12.2SS
12.4	Partner journeys: facility/service management, bookings, settlements	Srvin	08 Feb 27	19 Mar 27	30	7.4, 12.1
12.5	Web parity for 2A features (identity/roles, preferences, cancellation, waitlist)	Srvin	08 Mar 27	26 Mar 27	15	9.4, 7.8, 8.7
12.6	Cross-browser, responsive & accessibility testing; SEO for public pages	Srvin	22 Mar 27	02 Apr 27	10	12.5SS
12.7	◆ Web application build complete	Srvin	02 Apr 27	02 Apr 27	0	12.2, 12.3, 12.4, 12.5, 12.6
13 Release 2A.3 — Transaction Ledger + Web Application (Phase 2A complete) (05 Apr 27 – 02 Aug 27)						

WBS	Activity	Owner	Start	Finish	Days	Predecessors
13.1	SIT, end-to-end regression, performance test & VAPT (pre-go-live pen test)	Srvin	05 Apr 27	16 Apr 27	10	11.7, 12.7, 8.6
13.2	UAT by SportSeek testers; defect fixes	Joint	19 Apr 27	30 Apr 27	10	13.1
13.3	◆ Go / No-Go 2A.3	SportSeek	03 May 27	03 May 27	0	13.2
13.4	◆ Release 2A.3 live — PHASE 2A COMPLETE	Joint	04 May 27	04 May 27	0	13.3
13.5	Hypercare	Srvin	04 May 27	04 Jun 27	24	13.4
13.6	KT-3: Ledger, Web application, full-platform operations	Srvin	04 May 27	21 May 27	14	13.4
13.7	Infrastructure operations runbook & transition plan (SOW 15.1)	Srvin	19 Apr 27	21 May 27	25	13.1
13.8	90-day warranty — 2A.3	Srvin	04 May 27	02 Aug 27	65	13.4
13.9	◆ Phase 2A acceptance & KT checklist sign-off	SportSeek	28 May 27	28 May 27	0	13.6, 13.7
14 Continuous Support Obligations (20 Oct 26 – 18 Jan 27)						
14.1	Phase 1 production monitoring & bug fixes (SOW Section 16)	Srvin	20 Oct 26	04 Jun 27	164	2.14
14.2	90-day warranty — 2A.0 launch fixes	Srvin	20 Oct 26	18 Jan 27	65	2.14

9. Dependency management

9.1 Dependency types used

Type	Meaning	How it is managed
FS	Successor starts after predecessor finishes	Tracked in the schedule; a slip propagates automatically
SS	Successor starts once predecessor has started (e.g. UI one sprint ahead)	Lag reviewed at sprint planning
External (D-n)	Input from SportSeek or a SportSeek-contracted third party	Dated register (9.3); status at every weekly review; escalated 5 working days before the need-by date if not on track

9.2 Key internal (cross-stream) dependencies

#	From	To	Type	Why the dependency exists
I1	3.5 HLD sign-off	4.x Foundation; 5.1 Identity core	FS	Architecture decisions (IdP option, event bus, gateway) must be fixed before build
I2	3.7 Design system approval	3.9 Web UX; 12.1 Web shell	FS	SOW 14.2: UI/UX approved before development
I3	5.4 Role management	7.1 Service-type model; 6.4 Role-scoped preferences	FS	Partner types and notification scoping hang off roles on the shared identity
I4	4.3 Event bus	6.1 Notification core	FS	Notifications are triggered by domain events, not synchronous calls (SOW 6.1)
I5	7.1 Service-type model	8.1 Unified event/booking data model	FS	SOW 9.3 asks for a consistent data model supporting the generalisation
I6	6.5 Notification core	8.4 Waitlist; 8.5 Edit notifications	FS	Both features are notification-driven
I7	7.6 Route onboarding	11.6 Partner settlement view	FS	Settlements exist only for Route-linked partner accounts
I8	8.2 Cancellation/refund	11.5 Refund status tracker	FS	Ledger reflects refunds raised by the booking domain
I9	5.9 Identity complete	11.1 Ledger ingestion	FS	Ledger aggregates per person/partner identity (SOW 8.1)
I10	9.4 / 10.4 Releases	12.5 Web parity for 2A features	FS	Web gets 2A features once APIs are released and stable
I11	11.7, 12.7, 8.6	13.1 2A.3 SIT & pen test	FS	Final release hardening needs all remaining scope complete

9.3 External dependency register (SportSeek and third parties)

ID	Dependency	Owner	Need-by	Unblocks	Impact if late
D1	Mutual NDA and SOW/PO executed	SportSeek	29 Sept 26	1.1	Start of all work
D2	Phase 1 source code, DB schema, API docs; cloud, repo, store-console and gateway dashboard access	SportSeek	29 Sept 26	2.1, 3.1	Launch assessment cannot start

ID	Dependency	Owner	Need-by	Unblocks	Impact if late
D3	Named Product Owner (decisions within 1 working day during launch window); UAT testers for 15–19 Oct	SportSeek	29 Sept 26	2.2, 2.11	Launch gate and UAT slip
D4	Launch scope and go-live criteria sign-off	SportSeek	01 Oct 26	2.2	Freeze date at risk
D5	Expected launch peak concurrent users (load-test target)	SportSeek	05 Oct 26	2.6	Load test runs against an assumed figure
D6	Legal content: privacy policy, terms, DPDP notice text, store listing copy & assets	SportSeek	09 Oct 26	2.7, 2.10	Store submission blocked
D7	Apple App Store & Google Play developer accounts (SportSeek-owned) with release rights	SportSeek	29 Sept 26	2.10	Store submission blocked
D8	Requirement tool decision (JIRA or Trello) and workspace	SportSeek	05 Oct 26	3.2	Backlog managed off-tool temporarily
D9	Names and availability of SportSeek developers joining the squads	SportSeek	13 Nov 26	5.x onward	Capacity plan re-baselined
D10	Written confirmation that Razorpay Route (split settlement) is enabled for coach, physio and nutritionist partner categories	SportSeek / Razorpay	06 Nov 26	7.6, 11.x	Ledger compliance-light design cannot be confirmed (SOW 8.3)
D11	Refund & cancellation business policy (approver, timeframes, non-refundable items)	SportSeek	11 Dec 26	8.2, 8.3	Refund flows cannot be finalised
D12	Alert catalog confirmed; message templates supplied; new SMS templates registered on DLT	SportSeek	27 Nov 26	6.1, 6.7	Triggers ship without approved content
D13	WhatsApp Business Solution Provider contract; Meta-approved message templates	SportSeek	08 Jan 27	6.6	WhatsApp channel slips to next release
D14	Email provider and FCM/APNs credentials in SportSeek accounts	SportSeek	27 Nov 26	6.2, 6.3	Channel build blocked
D15	Decision: is the Transaction Ledger needed in User/Partner apps, or Admin + partner web only (SOW 8.1 open item)	SportSeek	06 Nov 26	3.8, 11.x	Ledger scope unconfirmed
D16	Warranty SLA numbers (acknowledge/resolve times) — SOW Section 16 open item	SportSeek	06 Nov 26	Support model	Default proposal applies
D17	UI/UX approvals turned around within 3 working days of submission	SportSeek	Rolling	3.7, 3.8	Build start for that module slips day-for-day
D18	Approval of account-merge rules for existing duplicate identities	SportSeek	11 Dec 26	5.7	Identity migration cannot execute
D19	Historical completed-event data files for import	SportSeek	05 Feb 27	8.6	Import tool tested with synthetic data only
D20	Phase 2A NFR targets: API p95 latency, peak concurrency, uptime SLA	SportSeek	06 Nov 26	3.4, 10.1, 13.1	Performance acceptance undefined

10. Critical path and schedule risk



Near-critical chain (about 10 working days of float): M2 Identity (to 8 Jan) → M5 Partner/Service + Razorpay Route onboarding (to 19 Feb) → M3 Ledger (to 19 Mar) → 2A.3 SIT. External gates on that chain: D10 Route confirmation (6 Nov), D18 account-merge rules (11 Dec).

Figure 3 — Phase 2A critical path

Launch critical path (2A.0): Access (D2) → Assessment (2.1) → Scope Gate (2.2) → Defect remediation (2.4) → Code freeze (2.9) → Store submission (2.10) and UAT (2.11) → Go/No-Go (2.13) → Launch (2.14). The store review window (2.10) is the least controllable step. That is why the release-candidate build is submitted on 14 Oct, with a four-working-day buffer before launch.

Phase 2A critical path (zero float): HLD sign-off → design-system approval (20 Nov) → web application build (30 Nov – 2 Apr), including web parity for the 2A.1/2A.2 features → 2A.3 SIT, performance and pen test → UAT → Go-live 4 May 2027. Any late design approval (D17) on web screens therefore moves the Phase 2A completion date. We will protect this path by staffing the web stream first when capacity is contested.

Near-critical chain (about 10 working days of float): Shared Identity (M2) → Partner/Service generalisation (M5) with Razorpay Route linked-account onboarding → Transaction Ledger (M3) → 2A.3 SIT. This chain carries the heaviest external dependencies (D10 Route confirmation, D18 account-merge rules), so it gets the same weekly scrutiny as the critical path.

10.1 Schedule risks on the critical path

Risk	Likelihood / impact	Mitigation built into this plan
Phase 1 assessment reveals more critical defects than fit before the 14 Oct freeze	Medium / High	Assessment in first 3 days; Scope Gate on 1 Oct prioritises fixes; joint Srivin + SportSeek developer remediation; de-scope option per journey
App store review exceeds buffer	Low–Medium / High	Submit RC on 14 Oct; pre-check store policies (privacy, account deletion, permissions) in 2.7; web/admin launch unaffected
Route not enabled for new partner categories (D10)	Medium / High	Confirmation needed by 6 Nov, before the 2A baseline; SOW 8.3 flags this as a costing prerequisite
Duplicate identities in Phase 1 data larger or messier than expected	Medium / Medium	Early duplicate report in 5.7; merge rules approved by 11 Dec (D18); migration dry-runs on Staging
Design approvals slower than 3 working days (D17), especially web screens on the critical path	Medium / High	UI produced one sprint ahead; fixed weekly design-review slot; web screens reviewed first
Festival and year-end holidays reduce capacity (Oct–Jan)	High / Low	Holiday calendar agreed at kick-off; S3 planned at reduced velocity

11. Milestones, gates and acceptance evidence

ID	Milestone / gate	Date	Decision owner	Acceptance evidence
1.2	Kick-off	29 Sep 2026	Joint	Governance charter, RACI, access checklist
2.2	Launch Scope Gate	01 Oct 2026	SportSeek	Assessment report; frozen launch scope; go-live criteria
2.9	Code freeze & RC	14 Oct 2026	Srvin	RC build, release notes, green CI pipeline
2.13	Go/No-Go (2A.0)	19 Oct 2026	SportSeek	UAT sign-off, VAPT retest clean (no critical/high), load-test report, runbook, store approval status
2.14	Public launch	20 Oct 2026	Joint	Production smoke test; monitoring dashboards green
3.5	HLD sign-off	13 Nov 2026	SportSeek	HLD document, ADRs, NFR targets
1.6	Phase 2A re-baseline	13 Nov 2026	SportSeek	Re-baselined plan with confirmed open items and milestone costing
3.7	Design system approval	20 Nov 2026	SportSeek	Approved design system and component library
4.6	M1 Foundation accepted	27 Nov 2026	SportSeek	IaC in SportSeek accounts; pipelines with quality gates; observability
9.4	Release 2A.1 live	27 Jan 2027	SportSeek	UAT sign-off; identity migration reconciliation report
10.4	Release 2A.2 live	16 Mar 2027	SportSeek	UAT sign-off; VAPT and performance reports
13.4	Release 2A.3 live — Phase 2A complete	04 May 2027	SportSeek	UAT sign-off; pen test (no open critical/high); ledger reconciliation vs gateway
13.9	Phase 2A acceptance	28 May 2027	SportSeek	All SOW 13 deliverables handed over; KT checklists signed

12. Sprint calendar

Sprint	Dates	Primary focus
S0	05 Oct – 13 Nov 2026	Discovery, HLD, design system, backlog (parallel to launch and hypercare)
S1	16 – 27 Nov 2026	Foundation (laC, CI/CD gates, event bus, observability); Identity core
S2	30 Nov – 11 Dec 2026	Identity: login refactor, account linking, roles; Notification core; Web shell
S3	14 – 25 Dec 2026	Identity: KYC reuse, profile; Push & Email; Web user journeys (reduced capacity — year-end)
S4	28 Dec 2026 – 08 Jan 2027	Account reconciliation & migration; preferences; service-type model
S5	11 – 22 Jan 2027	2A.1 SIT/UAT; WhatsApp; facility migration; cancellation & refund
S6	25 Jan – 05 Feb 2027	2A.1 go-live & KT-1; partner onboarding (new types); alert catalog; tournament refunds
S7	08 – 19 Feb 2027	Route onboarding; waitlist; edit notifications; Ledger ingestion; web partner journeys
S8	22 Feb – 05 Mar 2027	2A.2 SIT/perf/VAPT; Ledger APIs & admin screens; import tools
S9	08 – 19 Mar 2027	2A.2 UAT & go-live; exports; refund tracker; partner settlement view
S10	22 Mar – 02 Apr 2027	Web parity, browser/accessibility testing; KT-2 close
S11	05 – 16 Apr 2027	2A.3 SIT, end-to-end regression, performance and pen test
UAT	19 – 30 Apr 2027	2A.3 UAT; go-live 4 May; hypercare and KT-3 to 4 Jun

13. Resource plan, loading and technical skills

This section shows who Srivin will staff, with which technical skills, and when. It is sized to the schedule in Sections 7–8 and to SportSeek's confirmed technology stack: **React Native** mobile apps, a **.NET** back end and **PostgreSQL**. Loading is shown as monthly average full-time equivalents (FTE). October includes mobilisation from 28 September. Final names, CVs and rates will be in the commercial proposal. SportSeek developers and testers (Section 13.6) are in addition to these numbers.

13.1 Technology stack and the skills it demands

Layer	Technology	Skills we staff for
Mobile apps (User, Partner)	React Native (TypeScript), iOS and Android	OIDC/PKCE login on mobile, push (FCM/APNs), deep links and app-switch handling, schema-driven onboarding forms, store release engineering, minimum-version enforcement
Back end (modular monolith)	.NET — ASP.NET Core Web API, C#, EF Core with Npgsql	Domain module boundaries, OIDC identity service, transactional outbox and messaging, Razorpay payments/refunds/Route and webhooks, background scheduling, idempotent APIs
Database	PostgreSQL (schema per domain)	Expand/contract migrations, JSONB with schema validation, exclusion constraints against double-booking, geospatial radius search, query tuning, identity de-duplication and data migration
Web application & Admin Portal	React + TypeScript (Next.js recommended; ADR-05 in the Technical Approach)	Server-rendered public pages for SEO, shared design tokens with the React Native apps, data-heavy admin screens (ledger filters, sorting, exports), WCAG 2.1 AA
Quality engineering	xUnit + Testcontainers (.NET), Jest / React Native Testing Library, Detox or Maestro (mobile), Playwright (web), Postman/Newman (API), k6 or JMeter (load)	Automation in CI, regression packs for Phase 1 journeys, payment and refund test scenarios in Razorpay test mode
Platform & operations	SportSeek-owned cloud, CI/CD and managed PostgreSQL	Infrastructure as code, .NET and React Native build pipelines (Fastlane), OpenTelemetry observability, secrets management, backup/restore drills

13.2 Team composition and technical skills

Role	Seniority	Peak FTE	Person-months	Key technical skills	Tools
Delivery Manager / TPM	Senior (12+ yrs)	1	8.25	Hybrid agile delivery of multi-squad programmes; integrated planning, critical-path and dependency management; RAID; stakeholder and steering management; change control; release governance	JIRA / Trello, MS Project or equivalent, Confluence-style wiki
Scrum Master	Mid–Senior (6+ yrs)	1	6.5	Scrum facilitation across 4 squads; sprint metrics (velocity, burndown, predictability); impediment removal; scrum-of-scrums	JIRA / Trello boards and reports
Solution Architect (.NET / PostgreSQL)	Senior (12+ yrs)	1	7.25	ASP.NET Core modular-monolith and domain-driven design; PostgreSQL data architecture; OAuth2 / OIDC identity design; event-driven integration (transactional outbox, message brokers); payment-gateway architecture incl. Razorpay Route split settlement; React Native client architecture; OWASP ASVS; DPDP-aligned data design	C4 / architecture diagrams, ADRs, SportSeek cloud platform services
Business Analyst	Mid–Senior (6+ yrs)	2	12.5	Requirement workshops; user stories with Given/When/Then acceptance criteria; booking, events, payments/refunds and partner-onboarding domains; process and state modelling; SOW traceability; UAT scenario design	JIRA / Trello, BPMN / flow diagrams
UX / UI Designer	Mid–Senior (5+ yrs)	2	10	Atomic design systems (tokens → atoms → templates); mobile (iOS/Android) and responsive web UI; usability research and testing; accessibility (WCAG 2.1 AA); prototyping; developer hand-off	Figma or tool agreed with SportSeek

Role	Seniority	Peak FTE	Person-months	Key technical skills	Tools
.NET Tech Lead	Senior (10+ yrs)	2	13	C# / ASP.NET Core Web API; EF Core with Npgsql; modular boundaries and architecture tests; OIDC server/client implementation (e.g. OpenIddict or ASP.NET Core Identity); background jobs and scheduling; idempotency and webhook handling; code review and mentoring	xUnit, Testcontainers for .NET, NetArchTest / ArchUnitNET, OpenAPI tooling
.NET Backend Engineer	Mid (4–8 yrs)	4	24	C# / ASP.NET Core; EF Core + Npgsql; LINQ and SQL; REST APIs with OpenAPI; integration with Razorpay (payments, refunds, Route, webhooks), SMS, WhatsApp BSP, FCM/APNs and email; messaging consumers; unit and integration testing	xUnit, Testcontainers, Postman
PostgreSQL Database Engineer	Senior (8+ yrs)	1	4.75	Schema-per-domain design; EF Core migrations with expand/contract; JSONB with schema validation; exclusion constraints (btree_gist) for double-booking prevention; geospatial radius queries; indexing and query tuning (EXPLAIN ANALYZE); backup / point-in-time recovery; identity de-duplication and data-migration scripts; reconciliation SQL	psql, pg_stat_statements, PostGIS where used
React Native Lead	Senior (8+ yrs)	1	7	React Native with TypeScript for iOS and Android; navigation, state and API layers; native modules; OIDC with PKCE on mobile (e.g. react-native-app-auth); push notifications (FCM/APNs, e.g. React Native Firebase); deep links / universal links and app-switch handling; minimum-version enforcement; store release management	Fastlane, Xcode, Android Studio, crash and performance monitoring
React Native Engineer	Mid (4–7 yrs)	2	10.5	React Native + TypeScript; REST integration; schema-driven dynamic forms (partner onboarding); offline/error states; accessibility; unit and component testing; device/OS compatibility fixes	Jest, React Native Testing Library, Detox or Maestro
Web Front-end Lead (React)	Senior (8+ yrs)	1	6	React + TypeScript; Next.js server rendering for SEO-relevant public pages; shared design tokens / component library with the React Native apps; OIDC for web clients; performance (Core Web Vitals); WCAG 2.1 AA	Next.js, Storybook, Playwright
Web Front-end Engineer (React)	Mid (3–6 yrs)	2	9.5	React + TypeScript; responsive layouts; forms and validation; API integration; admin and partner web screens incl. ledger tables, filters, sorting and exports	Next.js, Playwright, Jest
QA Lead (Automation)	Senior (8+ yrs)	1	8.25	Test strategy and quality gates; automation architecture for API, React Native and web; CI integration; SIT and regression planning; defect governance; UAT support	Playwright, Detox / Maestro / Appium, Postman / Newman, xUnit
QA Engineer	Mid (3–6 yrs)	2	13.5	Functional and regression testing on iOS, Android and web; API testing; payment, refund, waitlist and notification test scenarios using Razorpay test mode; test-data management; automated test authoring	Postman, Playwright, device farm / physical devices
DevOps / SRE Engineer	Senior (7+ yrs)	1.5	9	Infrastructure as code in SportSeek's cloud; CI/CD for .NET services and React Native builds; managed PostgreSQL operations; containers; observability (OpenTelemetry for .NET, logs, metrics, alerting); secrets management; backup/restore drills; release automation and on-call	Terraform or cloud-native IaC, SportSeek's CI platform, Fastlane
Security Engineer (VAPT)	Senior (8+ yrs)	0.5	2.25	Web, API and mobile penetration testing (OWASP WSTG, MASTG); SAST/DAST/SCA tool set-up and triage; secure .NET and React Native review; remediation verification	SAST / DAST / SCA tooling, Burp Suite or equivalent
Performance Engineer	Mid–Senior (6+ yrs)	0.5	1.75	Load and stress test design; .NET API profiling; PostgreSQL query and connection-pool analysis; capacity recommendations	k6 or JMeter, dotnet-counters / dotnet-trace
Total			154		

13. Resource plan (continued)

13.3 Monthly resource loading (FTE)

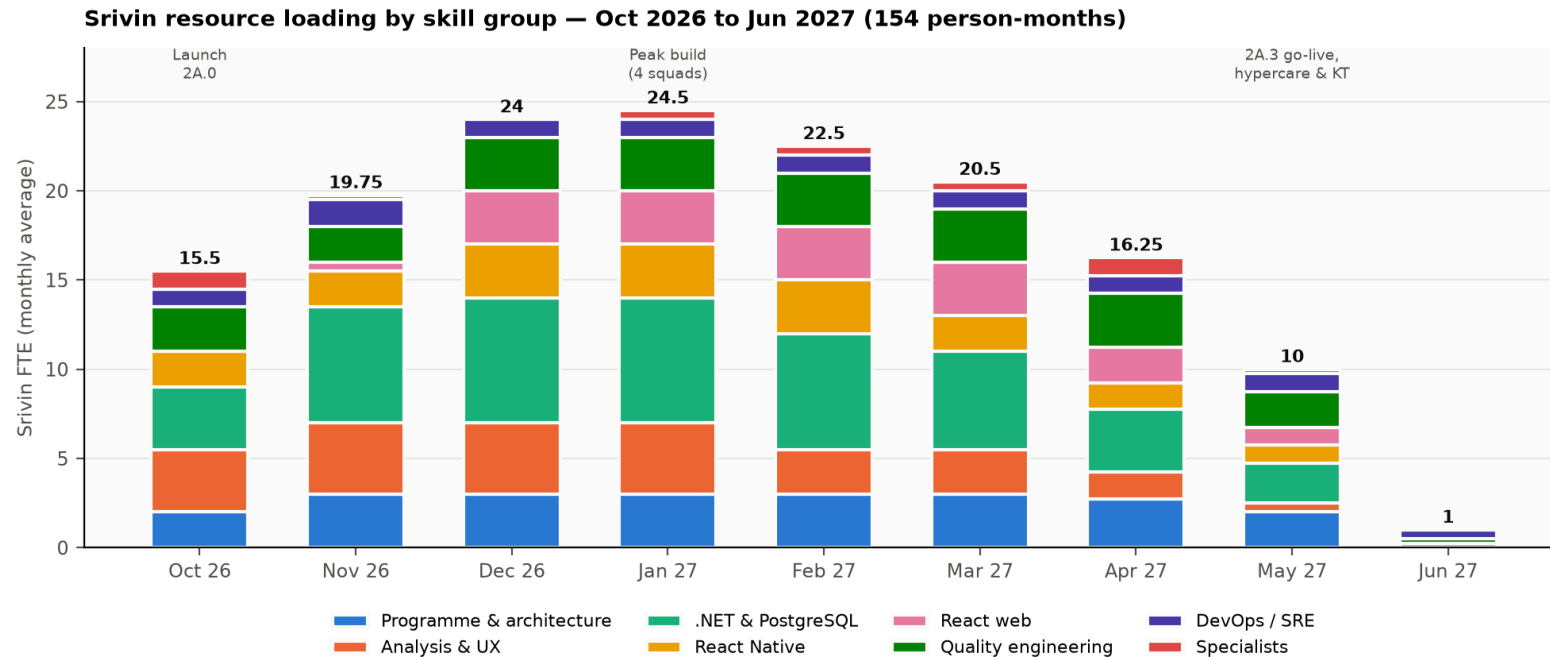


Figure 4 — Srvin resource loading by skill group

Role	Oct 26	Nov 26	Dec 26	Jan 27	Feb 27	Mar 27	Apr 27	May 27	Jun 27	Person-months
Delivery Manager / TPM	1	1	1	1	1	1	1	1	0.25	8.25
Scrum Master	—	1	1	1	1	1	1	0.5	—	6.5
Solution Architect (.NET / PostgreSQL)	1	1	1	1	1	1	0.75	0.5	—	7.25
Business Analyst	2	2	2	2	1.5	1.5	1	0.5	—	12.5
UX / UI Designer	1.5	2	2	2	1	1	0.5	—	—	10
.NET Tech Lead	1	2	2	2	2	2	1	1	—	13
.NET Backend Engineer	2	4	4	4	4	3	2	1	—	24

Role	Oct 26	Nov 26	Dec 26	Jan 27	Feb 27	Mar 27	Apr 27	May 27	Jun 27	Person-months
PostgreSQL Database Engineer	0.5	0.5	1	1	0.5	0.5	0.5	0.25	—	4.75
React Native Lead	1	1	1	1	1	1	0.5	0.5	—	7
React Native Engineer	1	1	2	2	2	1	1	0.5	—	10.5
Web Front-end Lead (React)	—	0.5	1	1	1	1	1	0.5	—	6
Web Front-end Engineer (React)	—	—	2	2	2	2	1	0.5	—	9.5
QA Lead (Automation)	1	1	1	1	1	1	1	1	0.25	8.25
QA Engineer	1.5	1	2	2	2	2	2	1	—	13.5
DevOps / SRE Engineer	1	1.5	1	1	1	1	1	1	0.5	9
Security Engineer (VAPT)	0.5	0.25	—	0.25	0.25	0.25	0.5	0.25	—	2.25
Performance Engineer	0.5	—	—	0.25	0.25	0.25	0.5	—	—	1.75
Total Srivin FTE	15.5	19.75	24	24.5	22.5	20.5	16.25	10	1	154

How the loading follows the plan: in October the launch squad (about 11 FTE) runs alongside the discovery cell (architect, analysts, UX). From 16 November the four build squads ramp up to a peak of about 24 FTE in December–January, when Identity, Notifications, Partner/Service, Booking hardening and the Web application are all in flight. From April the team tapers through 2A.3 testing, go-live, hypercare and KT, leaving a small core for closure in early June. The ramp-down is deliberate: as Srivin engineers roll off, SportSeek developers who have worked in the squads take over ownership (Section 13.7).

13.4 Squad composition at peak build (Dec 2026 – Mar 2027)

Squad	Scope (WBS)	Srivin members	SportSeek members
A — Platform & Identity	4 Foundation, 5 Shared Identity; then 11 Ledger APIs	.NET Tech Lead, .NET Backend Engineer, React Native Engineer, QA Engineer (shared with C), PostgreSQL Database Engineer (shared)	1 .NET developer (recommended)
B — Partner & Booking	7 Partner/Service model, 8 Booking hardening	.NET Tech Lead, .NET Backend Engineer, React Native Lead, React Native Engineer, QA Engineer	1 .NET or React Native developer (recommended)
C — Notifications & Ledger	6 Notification platform, 11 Transaction Ledger	2 .NET Backend Engineers, QA Engineer (shared with A)	1 .NET developer (recommended)
D — Web Application	12 Web application; Admin Portal screens for 7 and 11	Web Front-end Lead, 2 Web Front-end Engineers	1 React developer (recommended)
Cross-squad	All	Delivery Manager, Scrum Master, Solution Architect, 2 Business Analysts, 2 UX/UI Designers, QA Lead, DevOps/SRE, Security and Performance Engineers (per release)	Product Owner, tech reviewer, ops lead

13.5 Resource-to-WBS assignment matrix

● = primary responsibility (does most of the work); ○ = supporting or reviewing. Columns are the Level 1 WBS elements in Section 6.1.

Role	1 PM	2 Launch	3 Design	4 Found.	5 Identity	6 Notif.	7 Partner	8 Booking	9 Rel 2A.1	10 Rel 2A.2	11 Ledger	12 Web	13 Rel 2A.3	14 Support
Delivery Manager / TPM	●	●	○	○	○	○	○	○	●	●	○	○	●	○
Scrum Master	○			●	●	●	●	●	○	○	●	●	○	
Solution Architect (.NET / PostgreSQL)	○	●	●	●	●	●	●	○	○	○	●	○	●	○
Business Analyst		○	●	○	●	○	●	●	○	○	●	○	○	
UX / UI Designer			●		○	○	○	○				○	●	
.NET Tech Lead		●	○	●	●	○	●	●	○	○	○	○	○	●
.NET Backend Engineer		●	○	●	●	●	●	●			●			●
PostgreSQL Database Engineer		○	○	○	●		●	●			●		○	
React Native Lead		●	○		●	●	●	○	○	○			○	●
React Native Engineer		●			●	○	●	●						○
Web Front-end Lead (React)			○								○	●	○	
Web Front-end Engineer (React)											●	●		
QA Lead (Automation)	○	●	○	○	○	○	○	○	●	●	○	○	○	●
QA Engineer		●			●	●	●	●	●	●	●	●	●	
DevOps / SRE Engineer		●		●	○	○	○	○	●	●	○	○	●	●
Security Engineer (VAPT)		●							○	●			●	
Performance Engineer		●								●			●	

13. Resource plan (continued)

13.6 SportSeek-provided resources

Role	Number	When	Skills / responsibilities
Product Owner	1 (named)	Throughout; decisions within 1 working day during the launch window	Backlog priority, story acceptance, SOW open-item decisions (SOW \$5)
Technical reviewer / architect	1 (part-time)	Design authority, HLD/LLD reviews	.NET and PostgreSQL familiarity with Phase 1; review and approve designs
SportSeek developers	4 recommended (1 per squad); number to be confirmed (D9)	From Sprint 1 (16 Nov 2026)	.NET, React Native or React, as per squad (Section 13.4); full squad members
UAT testers	2 recommended	15–19 Oct 2026; Jan, Mar and Apr 2027 UAT windows	Business scenario testing across User, Partner, Admin and Web
Operations lead	1	From KT-0; co-operate stage from 2A.2	Receives infrastructure handover (SOW \$15.1)
Legal / compliance contact	As needed	Launch (by 9 Oct) and DPDP reviews	Privacy policy, terms, DPDP notice, refund policy

13.7 Onboarding, continuity and roll-off

- **Launch squad on day 1:** named engineers with React Native, .NET and PostgreSQL experience start on 28–29 Sep, so the Phase 1 assessment begins the moment access is granted (D2).
- **Key-person continuity:** the Delivery Manager, Solution Architect, .NET Tech Leads, React Native Lead and QA Lead stay for the full engagement. Any change needs SportSeek notice and a two-week overlap handover.
- **Ramp-up:** build squads onboard in the week of 9 Nov with Phase 1 code walkthroughs, environment set-up and pairing on HLD spikes, so Sprint 1 starts productive.
- **Skills coverage:** every critical skill (.NET identity/OIDC, PostgreSQL migrations, React Native release engineering, Razorpay integration) is held by at least two people across Srivin and SportSeek by the end of 2A.1.
- **Roll-off:** engineers roll off only after the KT checklist for their module is signed (SOW \$12.2), and SportSeek developers take over module ownership as Srivin capacity reduces from April 2027.

14. Baseline control and re-planning rules

- **Baselines:** this plan is Baseline 0. Baseline 1 is set at the Phase 2A re-baseline (13 Nov 2026), once HLD and the open items (D10, D11, D15, D16, D20) are closed.
- **Tolerances:** a forecast slip of more than 5 working days on any go-live milestone, or more than 10 working days on any build milestone, is escalated to the Steering Committee with options.
- **Change:** scope changes follow SOW Section 18: a written request, then a Srivin impact assessment within 5 business days, then SportSeek approval and a baseline update.
- **Reporting:** a weekly status report shows milestone forecast vs baseline, the dependency register and RAID. A monthly Steering Committee reviews the critical path.
- **Tooling:** stories, test cases and acceptance criteria live in SportSeek's chosen tool (JIRA or Trello, SOW 13), and this schedule is kept in step with it.

Appendix A. SOW-to-WBS traceability

SOW reference	Requirement	WBS
3.1 Shared Identity; 7; 9.1	Unified accounts, account linking, roles, KYC reuse	5.1–5.9
3.1 Transaction Ledger; 8; 9.2	Ledger dashboard, statements, refund status, partner view	11.1–11.7
3.1 Booking/Events; 9.3	Harden Phase 1; cancellation, waitlist, edit alerts, data model, import tools	2.4, 8.1–8.7
3.1 Partner & Service; 9.4	Generalised service types, admin configuration	7.1–7.8
3.1 Notification; 10	Push, WhatsApp, Email; alert catalog	6.1–6.7
3.1 Web application	Web app for all existing functionality	12.1–12.7
6.2 NFRs	Security, performance, availability, DPDP, environments, observability	2.3, 2.5, 2.6, 4.x, 10.1, 13.1
12.1 M1	Foundation setup	2.3, 4.1–4.6
12.2 KT	KT after every milestone with checklist	2.16, 9.5, 10.5, 13.6
13 Deliverables	Code, HLD/LLD, stories/tests, API docs, ERD, architecture, UI files, test suite, CI/CD, runbook, user docs, KT	3.4, 3.6, 3.10, 4.2, 13.7, all build WPs
14 Acceptance	Technical and functional acceptance	9.1–9.3, 10.1–10.3, 13.1–13.3, 13.9
15.1 Infra transition	Operate-then-handoff runbook and plan	13.7
16 Warranty & support	90-day warranty per milestone; Phase 1 support	9.6, 10.6, 13.8, 14.1, 14.2
18 Change management	Change process	1.5
