

SRIVIN PLATFORMS

Delivery partner to RacingAhead / SportSeek

SportSeek — Unified Sports Ecosystem Platform

Work Breakdown Structure & Integrated Project Plan

Phase 2A, AI-native delivery: public launch on 20 October 2026, then two features every month to Phase 2A completion on 23 March 2027

Document control	
Document	SRV-SPS-2A-PLN-001
Programme	SportSeek Phase 2 — Phase 2A (Harden & Unify)
Client	RacingAhead / SportSeek, Hyderabad
Prepared by	Srvin Platforms — Technical Programme Management Office
Version / date	v2.0 (AI-native release train) — 27 September 2026
Status	Issued for client review — supersedes v1.0
Reference baseline	SportSeek Phase 2 SOW v1.0 (15 Jul 2026); SportsSeek App High Level Requirements
Classification	Confidential — RacingAhead / SportSeek and Srvin Platforms only

Contents

- 1. Purpose and conventions
- 2. Executive summary
- 3. The AI-native delivery approach in brief
- 4. Feature catalogue: 12 features in 6 monthly releases
- 5. Date feasibility and release-train rules
- 6. Planning basis and assumptions
- 7. Work Breakdown Structure (WBS) and WBS dictionary
- 8. Integrated schedule
- 9. Detailed activity schedule
- 10. Dependency management
- 11. Critical path and schedule risk
- 12. Milestones, gates and acceptance evidence
- 13. Anatomy of a monthly release
- 14. Resource plan: AI-native pod, loading and technical skills
- 15. Baseline control and re-planning rules
- Appendix A. SOW-to-WBS traceability

1. Purpose and conventions

This is the integrated project plan for Phase 2A of the SportSeek programme, prepared by Srivin Platforms as delivery partner to RacingAhead / SportSeek. It breaks the Phase 2A scope in the SportSeek Phase 2 SOW into **12 customer-facing features delivered in 6 monthly releases**, schedules every work package, and dates every dependency on SportSeek and third parties.


Version 2.0 replaces the conventional plan in v1.0 with Srivin's **AI-native delivery model**. A small senior pod uses AI coding, testing and documentation agents under strict human review, so SportSeek gets features in production every month rather than every quarter. Where the SOW leaves an item open (marked  in the SOW), this plan does not assume an answer; it records a dated SportSeek decision (Section 10.3).

Companion document	Purpose
SRV-SPS-2A-DLM-002 Project Delivery Model	How the AI-native release train runs: AI-augmented lifecycle, cadence, governance, AI guardrails, quality, KT and support
SRV-SPS-2A-TAD-003 Technical Approach	Architecture on React Native / .NET / PostgreSQL, per-feature design, and the AI-accelerated engineering approach
SRV-SPS-2A-PLN-001a Project Plan workbook (.xlsx)	Schedule, dependency register, milestones and resource loading in spreadsheet form

- **Dates** are IST calendar dates; durations are working days (Mon–Fri). Public and festival holidays are applied once the joint holiday calendar is agreed.
- **Owner**: "Srivin", "SportSeek" or "Joint" (both, Srivin driving). **Predecessors**: a bare ID is Finish-to-Start, "SS" is Start-to-Start, "D-n" is an external dependency.
- **R1–R6** are the monthly releases; **F1–F12** are the features. SOW milestone numbers M1–M6 are kept in the traceability appendix.

2. Executive summary

SportSeek came to Srivin for a faster go-to-market. This plan delivers it. **SportSeek goes public on 20 October 2026 with two new features on day one, and then receives two new features in production every month.** The full Phase 2A scope is live by **23 March 2027**, delivered by an AI-native pod of about 10 people.

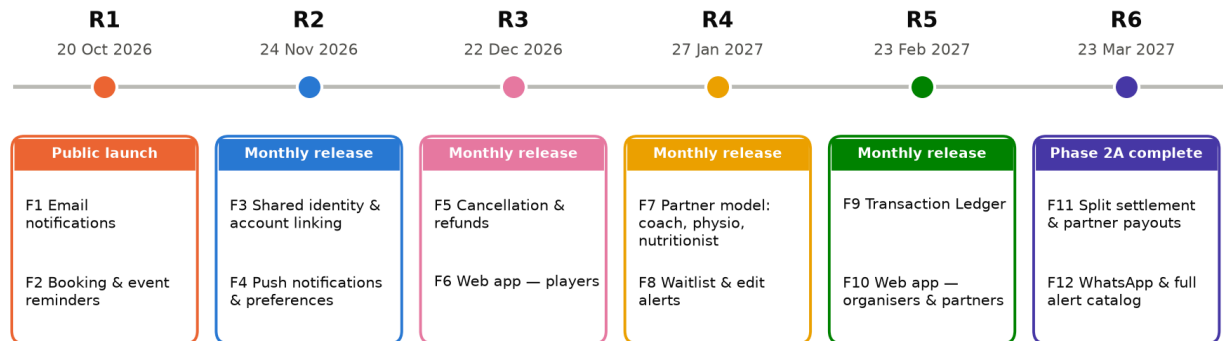

Fixed dates, flexible scope: a feature that is not release-ready rides the next train behind a feature flag. It never delays the train.

Figure 1 — Phase 2A release train: 6 releases, 12 features, one release every month

Release	Go-live	Features	SOW scope
R1	Tue 20 Oct 2026	Public launch of the hardened Phase 1 product + F1 Email notifications for all live alerts + F2 Booking & event reminders	Launch; M1 subset; M6 (part)
R2	Tue 24 Nov 2026	F3 Shared identity & account linking + F4 Push notifications & role-scoped preferences	M2; M6 (part)
R3	Tue 22 Dec 2026	F5 Cancellation & refunds + F6 Web app for players	M4 (part); Web app
R4	Wed 27 Jan 2027	F7 Generalised partner model (coach, physio, nutritionist) + F8 Waitlist & edit alerts	M5; M4 (part)
R5	Tue 23 Feb 2027	F9 Transaction Ledger + F10 Web app for organisers & partners	M3; Web app
R6	Tue 23 Mar 2027	F11 Split settlement & partner payouts + F12 WhatsApp & full alert catalog — Phase 2A complete	M5/M3 (payouts); M6

2.1 What changes versus a conventional plan

The comparison below is against Srivin's own conventional estimate for the same scope (plan v1.0), not a market benchmark.

Measure	Conventional (v1.0)	AI-native (this plan)	Difference
First new feature in production	Jan 2027	20 Oct 2026 (launch day)	~3 months sooner
Release cadence	4 releases in 7 months	6 releases, one every month	Monthly value
Phase 2A complete	4 May 2027	23 Mar 2027	6 weeks sooner
Peak Srivin team	~24.5 FTE	~ 12 FTE (launch month); ~10.5 steady state	~55% smaller
Total Srivin effort	154 person-months	67.25 person-months	56% less
Knowledge transfer	2–4 weeks after each milestone	Continuous, with a signed checklist every release	No KT gaps

Key messages for the steering committee

- 1. Speed is designed in, not promised.** AI agents write most first-draft code, tests and documentation from approved specifications, and senior engineers review and own every change. That is why a 10-person pod can release two features a month.
- 2. We are explicit about what AI does not speed up:** SportSeek decisions, app-store review, UAT, penetration testing, and third-party approvals (Razorpay Route, DLT and WhatsApp templates). These are dated dependencies in Section 10.3. Each one is on SportSeek's side of the table and can move a feature to the next train.
- 3. Fixed dates, flexible scope.** Every release date is fixed. If a feature is not release-ready, it rides the next monthly train behind a feature flag and the train still leaves on time.
- 4. Day-one prerequisite:** SportSeek's approval of Srivin's AI tooling on its code (D21, by 29 Sep). Without it, the plan reverts to conventional pace and team size.

3. The AI-native delivery approach in brief

AI changes the economics of building software; it does not change who is accountable. Our model puts AI agents inside every engineering step and keeps a named senior engineer responsible for everything that merges. The full model is in the Project Delivery Model (SRV-SPS-2A-DLM-002). The planning consequences are below.

Where AI accelerates delivery	Where it does not, so the plan protects time for it
Reading and documenting the live Phase 1 code (architecture, ERD, API catalogue) in days instead of weeks	SportSeek decisions and approvals (scope, designs, refund policy, merge rules)
Drafting user stories, acceptance criteria, edge cases and UAT scripts from the SOW	App Store / Google Play review windows
Generating implementation code and unit tests from approved specifications	UAT by SportSeek testers
Generating API, regression and end-to-end tests; test data	Manual penetration testing (VAPT) before go-live
Porting existing mobile journeys to the web against the same APIs	Razorpay Route enablement, DLT template registration, WhatsApp template approval
Migration and reconciliation scripts; first-pass code review; living documentation	Production data migration windows and rehearsals

Planning assumption: AI-assisted build, test and documentation effort is planned at roughly 40–50% of our conventional estimate. No reduction is assumed for decisions, approvals, UAT or security testing. Actual velocity is measured from R2, and the plan is re-baselined at the R2 release review if needed (Section 15).

4. Feature catalogue: 12 features in 6 monthly releases

ID	Feature	What the user gets	Rel.	Depends on	SOW ref.
F1	Email notifications	Email alongside SMS for OTP-free alerts: booking, registration and payment confirmations	R1	D14 email provider	\$10.1–10.2
F2	Booking & event reminders	T-24h and T-2h reminders for bookings and events	R1	D12 templates / DLT	\$10.2
F3	Shared identity & account linking	One account across User and Partner apps; OTP-verified linking; multiple roles; KYC reused	R2	HLD (3.4)	\$7, \$9.1
F4	Push notifications & preferences	Push on iOS/Android; notification preferences per role	R2	F3 roles; D14 FCM/APNs	\$7.4, \$10
F5	Cancellation & refunds	Cancel bookings and tournament registrations; refunds to original payment method via the gateway	R3	D11 refund policy	\$8.2, \$9.3
F6	Web app — players	Venue search, availability, booking, event registration and payment on the web	R3	F3 login; design system	\$3.1
F7	Generalised partner model	Coach, physio and nutritionist partners onboard like facilities; new types enabled by admin configuration	R4	F3 roles	\$9.4
F8	Waitlist & edit alerts	Join a waitlist for full slots/tournaments; alerts when a published event changes	R4	F4 channels; F5 states	\$9.3, \$10.2
F9	Transaction Ledger	Admin payment history, detail, filters, sorting, PDF/CSV statements, refund tracker	R5	F3; F5; D15	\$8
F10	Web app — organisers & partners	Events, tournaments, scheduling, scoring, service and booking management on the web	R5	F6; F7	\$3.1
F11	Split settlement & partner payouts	Razorpay Route linked accounts for all partner types; partner settlement view on web	R6	F7; F9; D10	\$8.2–8.3
F12	WhatsApp & full alert catalog	WhatsApp channel and every SOW \$10.2 trigger live	R6	F4; D13	\$10

Enablers ship inside releases but are not counted as features: platform foundation (R2), reconciliation of existing duplicate accounts (R3), data import tools for completed events (R6), and the infrastructure operations runbook (R6).

5. Date feasibility and release-train rules

As at the date of this plan (Sunday 27 September 2026) there are 16 working days before 20 October 2026. R1 is feasible because it adds only two low-risk, back-end-led features to a hardened Phase 1 product. The AI-generated regression suite and AI-assisted assessment compress the hardening work into the available window.

Launch-date conditions

The 20 Oct date holds only if: **(a)** the NDA/SOW is executed and access to code, infrastructure, store consoles and the gateway dashboard is granted by **29 Sep**; **(b)** AI tooling is approved by **29 Sep** (D21); **(c)** launch scope is frozen at the Scope Gate on **1 Oct**; **(d)** legal content is supplied by **9 Oct**; **(e)** UAT testers are available **15–19 Oct**.

F1 and F2 need the email provider account and message templates by 5 Oct (D12, D14). If these are late, F1/F2 ship as a fast-follow within 2 weeks. The public launch itself is not delayed.

5.1 Release-train rules

- 1. Release dates are fixed** for the whole plan; they are the calendar SportSeek's marketing can plan around.
- 2. Scope flexes between trains.** A feature that misses its hardening entry criteria moves to the next train behind a feature flag. It is never forced into production.
- 3. Every release passes the same gates:** automated regression, security scans, UAT sign-off and Go/No-Go (Section 12). Security-sensitive releases (R2 identity, R3 refunds, R6 payouts) also get a targeted manual pen test, and R6 gets the full pre-completion VAPT.
- 4. Back-end changes can deploy continuously** behind flags; mobile store releases follow the monthly train.

6. Planning basis and assumptions

#	Assumption	If it does not hold
A1	Kick-off Tue 29 Sep 2026 with NDA and SOW/PO executed.	Launch at risk day-for-day
A2	Phase 1 source code, DB schema and API documentation provided before kick-off (SOW \$5).	Launch hardening slips
A3	All accounts are SportSeek-owned; Srivin works within them (SOW \$5, \$15).	Access requests on the critical path
A4	A named SportSeek Product Owner decides within 1 working day and approves UI within 2 working days.	Features ride the next train
A5	SportSeek testers run UAT in the hardening week of each release (3 days).	Release slips to next train
A6	Stack as confirmed: React Native mobile, .NET back end, PostgreSQL. React/Next.js proposed for web.	Skills mix re-planned
A7	SportSeek approves AI tooling under enterprise terms (no training on SportSeek code or data; no production personal data in prompts) (D21).	Plan reverts to conventional pace and team
A8	Razorpay is the gateway; Route split settlement will be integrated (SOW \$8.3 NOTE).	F11 re-planned via change request
A9	Ledger scope is Admin + partner settlement view on web (SOW \$8.1–8.2); any mobile ledger view is confirmed by D15.	Adds scope to a later train
A10	AI-assisted build effort planned at ~40–50% of conventional; no reduction for approvals, UAT, VAPT.	Re-baseline at R2 review
A11	Phase 2B/2C scope excluded; the same train can continue into Phase 2B from April 2027.	—

7. Work Breakdown Structure (WBS) and WBS dictionary

The WBS is organised by release, so each Level-1 element is something SportSeek can accept on its own. Every Phase 2A scope item in SOW §3.1 and every deliverable in SOW §13 maps to a work package (Appendix A).

7.1 WBS hierarchy (Levels 1–2)

L1	Element	Level-2 work packages
1	Programme Management & AI Delivery Governance	1.1 Mobilisation & AI toolchain · 1.2 Kick-off · 1.3 Train plan, RAID, AI policy · 1.4 Governance cadence · 1.5 Change control · 1.6 Closure
2	R1 — Public Launch + F1, F2	2.1 AI-assisted assessment · 2.2 Scope Gate · 2.3 Env/CI-CD · 2.4 AI-generated regression suite · 2.5 Defects · 2.6 Security & VAPT · 2.7 Load test · 2.8 Store & DPDP · 2.9 F1 · 2.10 F2 · 2.11 Freeze · 2.12 Store · 2.13 UAT · 2.14 Runbook · 2.15 Go/No-Go · 2.16 Launch · 2.17 Hypercare
3	Discovery, Architecture & Design	3.1 AI-generated as-is docs · 3.2 Story mapping · 3.3 HLD & ADRs · 3.4 HLD sign-off · 3.5 Design system · 3.6 Design approval · 3.7 Specs/UI/LLD one train ahead · 3.8 Open-item closure
4	Platform Foundation (M1)	4.1 IaC · 4.2 CI/CD gates incl. AI review · 4.3 Event bus, BFF, feature flags · 4.4 M1 acceptance
5	R2 — F3, F4	5.1 F3 Shared identity · 5.2 F4 Push & preferences · 5.3 Hardening & UAT · 5.4 Go-live · 5.5 Hypercare & KT
6	R3 — F5, F6	6.1 F5 Cancellation & refunds · 6.2 F6 Web (players) · 6.3 Account reconciliation · 6.4 Hardening · 6.5 Go-live · 6.6 Hypercare & KT
7	R4 — F7, F8	7.1 F7 Partner model · 7.2 F8 Waitlist & edit alerts · 7.3 Hardening · 7.4 Go-live · 7.5 Hypercare & KT
8	R5 — F9, F10	8.1 F9 Ledger · 8.2 F10 Web (organisers & partners) · 8.3 Hardening · 8.4 Go-live · 8.5 Hypercare & KT
9	R6 — F11, F12 & Phase completion	9.1 F11 Route payouts · 9.2 F12 WhatsApp & catalog · 9.3 Import tools · 9.4 Hardening & full VAPT · 9.5 Go-live · 9.6 Hypercare · 9.7 Ops runbook · 9.8 Final KT · 9.9 Acceptance
10	Continuous Support	10.1 Phase 1 production support · 10.2 90-day warranty per release

7.2 WBS dictionary — key work packages

WBS	Work package	Key deliverables	Completion / acceptance criteria	SOW
2.1	AI-assisted Phase 1 assessment	Codebase map, ERD, API inventory, dependency and security findings, defect triage, launch risks	Reviewed at the Scope Gate; each launch risk owned and decided	5, 16
2.4	AI-generated regression suite	Automated API and mobile regression covering every live Phase 1 journey	Suite green on the RC build; runs on every merge from then on	14.1
2.6	Security baseline	SAST, dependency, DAST reports; VAPT of launch surface; remediation log	No open critical/high findings at Go/No-Go	6.2
3.3	HLD & ADRs	Target architecture, ADRs, integration and security design, NFR targets	Signed off by SportSeek (3.4)	6, 13
3.7	Feature specs & LLD	Per feature: spec, API contract (OpenAPI), DB changes, UI frames, acceptance tests. The spec is the input the AI agents build from.	Approved by PO and architect before its train starts	9, 13
5.1	F3 Shared identity	OIDC clients per app; OTP-verified linking; roles; KYC reuse	Existing User App phone/email registering on Partner App links to the same identity, with no duplicate	7.3, 9.1
6.1	F5 Cancellation & refunds	Policy rules; gateway refund API with idempotency; state machine; notifications	No double refund under retry; Phase 1 regression green	8.2, 9.3
6.3	Account reconciliation	Duplicate report; approved merge rules; migration & rollback scripts	Dry-run reconciles 100% of records; SportSeek approves (D18)	7.3, 17

WBS	Work package	Key deliverables	Completion / acceptance criteria	SOW
7.1	F7 Partner model	Service-type registry; admin configuration; facility migration; verification per type	New type enabled without code; facility partners unaffected	9.4
8.1	F9 Transaction Ledger	Ingestion + reconciliation; admin screens; exports; refund tracker	Every gateway transaction appears within the sync window; exports match gateway exactly	8.2
9.1	F11 Split settlement	Route linked accounts for all partner types; settlement view on web	Test partners of every type receive split settlement in Razorpay test mode	8.3
6.2, 8.2	Web application	React/Next.js web app for players (R3), organisers & partners (R5)	Parity checklist vs mobile signed; browser and accessibility checks pass	3.1
per release	KT checklist	AI-maintained docs, walkthrough, checklist per release	Checklist signed within 5 working days of each go-live	12.2

8. Integrated schedule

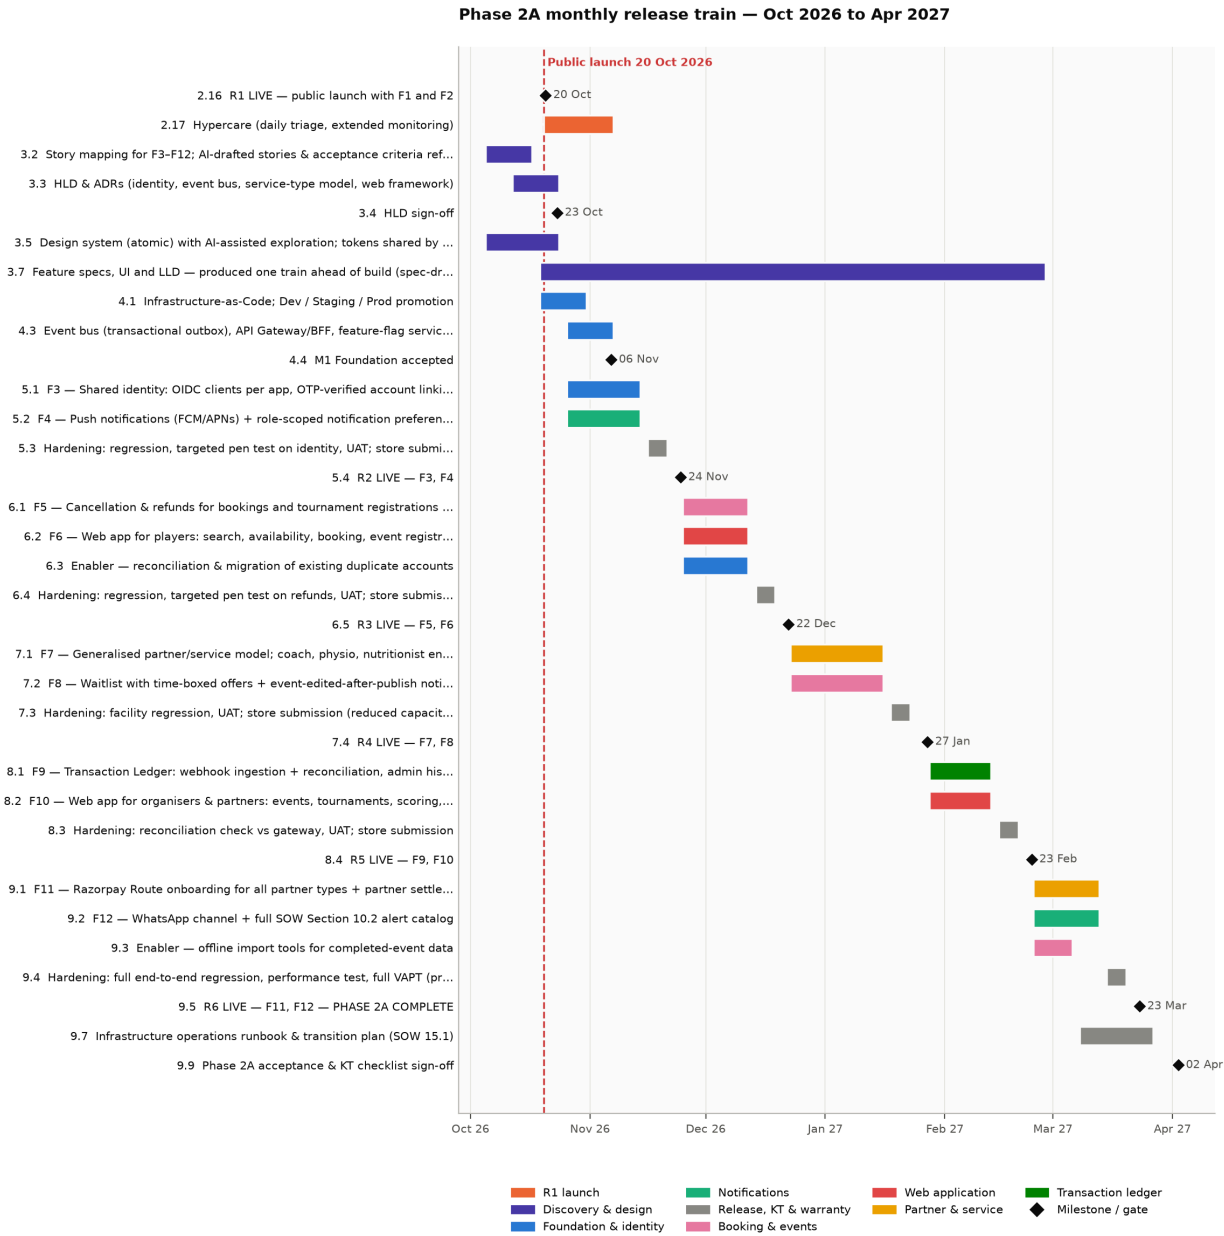


Figure 2 — Phase 2A monthly release train (summary level; all activities in Section 9)

8. Integrated schedule (continued)

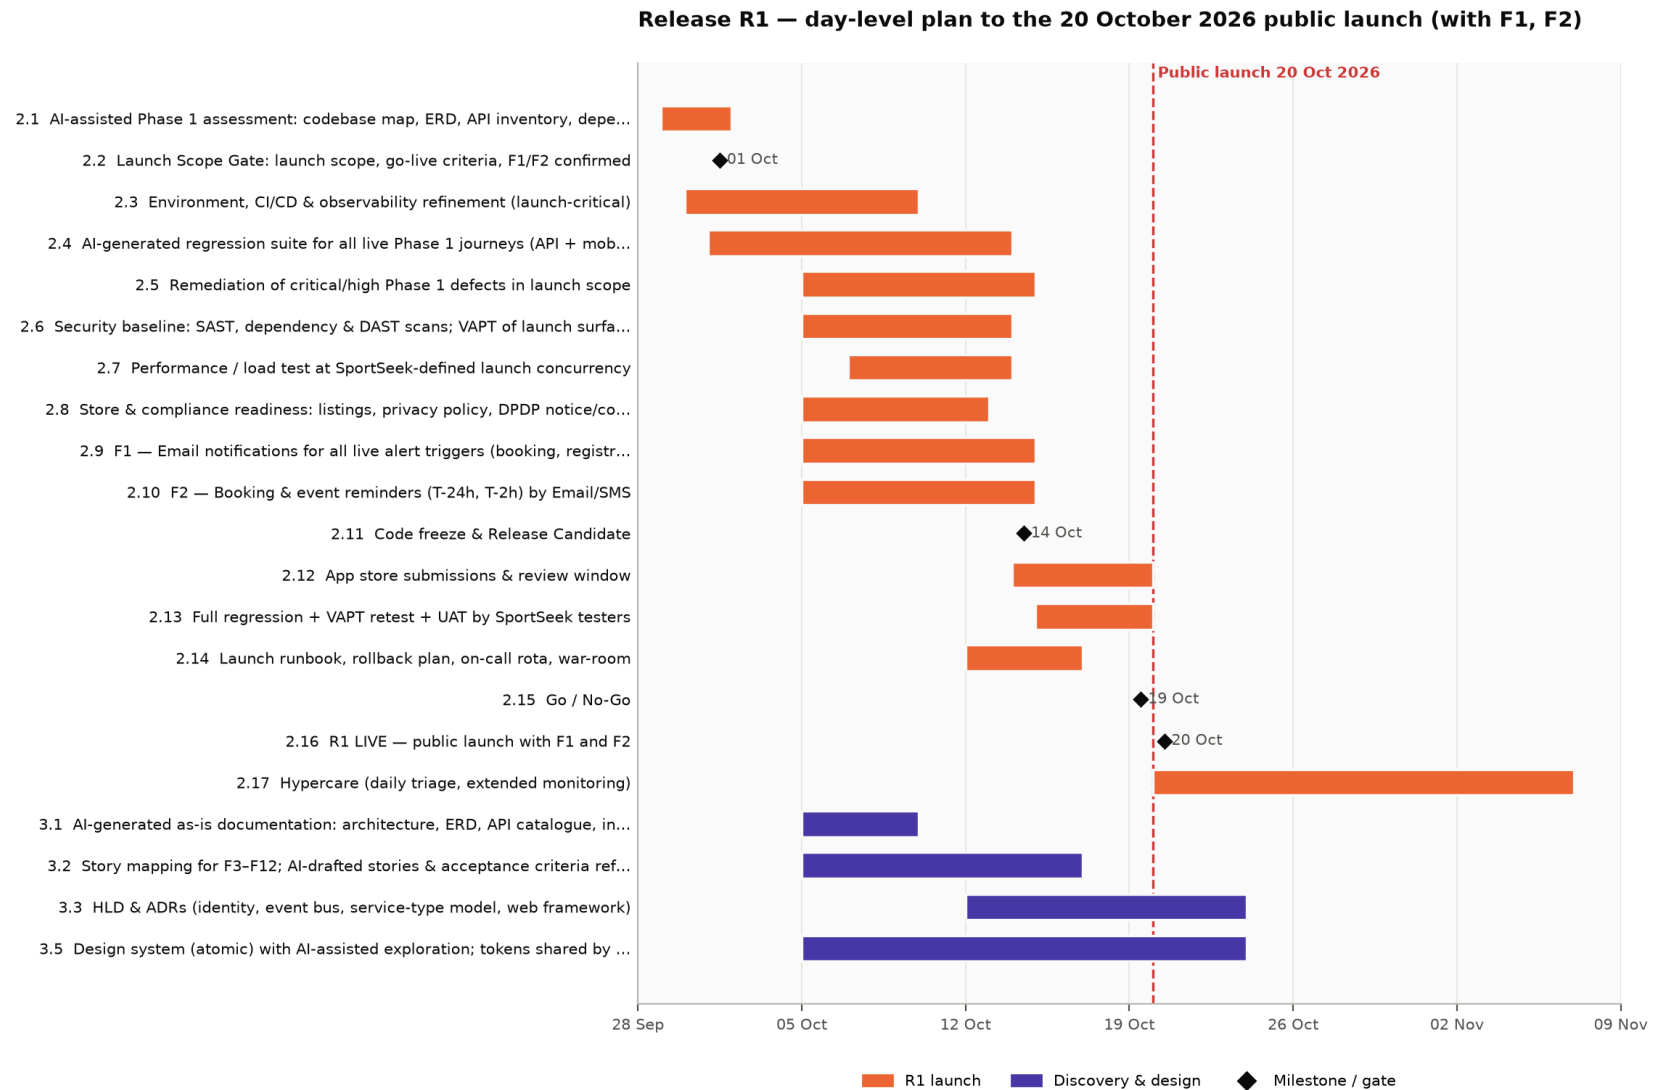


Figure 3 — Release R1: day-level plan to the 20 October 2026 public launch

9. Detailed activity schedule

Every activity with owner, dates, working-day duration and predecessors. The same data is in the workbook (SRV-SPS-2A-PLN-001a).

WBS	Activity	Owner	Start	Finish	Days	Predecessors
1 Programme Management & AI Delivery Governance (28 Sept 26 – 09 Apr 27)						
1.1	Mobilisation: NDA, SOW/PO, access; AI toolchain set up under SportSeek-approved terms (D21)	Joint	28 Sept 26	30 Sept 26	3	—
1.2	◆ Kick-off workshop (SportSeek + Srivin)	Joint	29 Sept 26	29 Sept 26	0	1.1SS
1.3	Release-train plan, RAID log, governance charter, AI usage policy	Srivin	29 Sept 26	02 Oct 26	4	1.2
1.4	Governance cadence: daily stand-up, weekly demo & status, monthly release review / steering	Srivin	30 Sept 26	09 Apr 27	138	1.2
1.5	Change control (SOW Section 18) — ongoing; scope flexes between trains, dates do not	Joint	30 Sept 26	09 Apr 27	138	1.2
1.6	Phase 2A closure: completion report, lessons learned, Phase 2B readiness	Joint	05 Apr 27	09 Apr 27	5	9.9
2 Release R1 — Public Launch + F1, F2 (20 Oct 2026) (29 Sept 26 – 06 Nov 26)						
2.1	AI-assisted Phase 1 assessment: codebase map, ERD, API inventory, dependency & security scan, defect triage	Srivin	29 Sept 26	01 Oct 26	3	1.2, D2
2.2	◆ Launch Scope Gate: launch scope, go-live criteria, F1/F2 confirmed	SportSeek	01 Oct 26	01 Oct 26	0	2.1
2.3	Environment, CI/CD & observability refinement (launch-critical)	Srivin	30 Sept 26	09 Oct 26	8	1.2
2.4	AI-generated regression suite for all live Phase 1 journeys (API + mobile)	Srivin	01 Oct 26	13 Oct 26	9	2.1SS
2.5	Remediation of critical/high Phase 1 defects in launch scope	Joint	05 Oct 26	14 Oct 26	8	2.2
2.6	Security baseline: SAST, dependency & DAST scans; VAPT of launch surface	Srivin	05 Oct 26	13 Oct 26	7	2.2
2.7	Performance / load test at SportSeek-defined launch concurrency	Srivin	07 Oct 26	13 Oct 26	5	2.3SS, D5
2.8	Store & compliance readiness: listings, privacy policy, DPDP notice/consent, account deletion	Joint	05 Oct 26	12 Oct 26	6	2.2, D6
2.9	F1 — Email notifications for all live alert triggers (booking, registration, payment)	Srivin	05 Oct 26	14 Oct 26	8	2.2, D14
2.10	F2 — Booking & event reminders (T-24h, T-2h) by Email/SMS	Srivin	05 Oct 26	14 Oct 26	8	2.2, D12
2.11	◆ Code freeze & Release Candidate	Srivin	14 Oct 26	14 Oct 26	0	2.5, 2.9, 2.10
2.12	App store submissions & review window	Joint	14 Oct 26	19 Oct 26	4	2.11, 2.8
2.13	Full regression + VAPT retest + UAT by SportSeek testers	Joint	15 Oct 26	19 Oct 26	3	2.11
2.14	Launch runbook, rollback plan, on-call rota, war-room	Srivin	12 Oct 26	16 Oct 26	5	2.3
2.15	◆ Go / No-Go	SportSeek	19 Oct 26	19 Oct 26	0	2.12, 2.13, 2.14
2.16	◆ R1 LIVE — public launch with F1 and F2	Joint	20 Oct 26	20 Oct 26	0	2.15
2.17	Hypercare (daily triage, extended monitoring)	Srivin	20 Oct 26	06 Nov 26	14	2.16

WBS	Activity	Owner	Start	Finish	Days	Predecessors
3 Discovery, Architecture & Design (AI-assisted, runs alongside launch) (05 Oct 26 – 26 Feb 27)						
3.1	AI-generated as-is documentation: architecture, ERD, API catalogue, integration map	Srvin	05 Oct 26	09 Oct 26	5	2.1
3.2	Story mapping for F3–F12; AI-drafted stories & acceptance criteria refined with PO	Joint	05 Oct 26	16 Oct 26	10	3.1SS, D8
3.3	HLD & ADRs (identity, event bus, service-type model, web framework)	Srvin	12 Oct 26	23 Oct 26	10	3.1
3.4	◆ HLD sign-off	SportSeek	23 Oct 26	23 Oct 26	0	3.3
3.5	Design system (atomic) with AI-assisted exploration; tokens shared by mobile & web	Srvin	05 Oct 26	23 Oct 26	15	3.2SS
3.6	◆ Design system approval	SportSeek	23 Oct 26	23 Oct 26	0	3.5
3.7	Feature specs, UI and LLD — produced one train ahead of build (spec-driven development)	Joint	19 Oct 26	26 Feb 27	95	3.3SS
3.8	Closure of SOW open items (ledger visibility, alert catalog, SLAs, NFRs, refund policy, Route)	SportSeek	05 Oct 26	08 Jan 27	70	D10, D11, D15, D16, D20
4 Platform Foundation (M1) — built in the first build cycle (19 Oct 26 – 06 Nov 26)						
4.1	Infrastructure-as-Code; Dev / Staging / Prod promotion	Srvin	19 Oct 26	30 Oct 26	10	3.3SS
4.2	CI/CD quality gates incl. AI code review, SAST, dependency & secret scanning, coverage	Srvin	19 Oct 26	30 Oct 26	10	3.3SS
4.3	Event bus (transactional outbox), API Gateway/BFF, feature-flag service	Srvin	26 Oct 26	06 Nov 26	10	3.4
4.4	◆ M1 Foundation accepted	SportSeek	06 Nov 26	06 Nov 26	0	4.1, 4.2, 4.3
5 Release R2 — F3 Shared Identity, F4 Push & Preferences (24 Nov 2026) (26 Oct 26 – 30 Nov 26)						
5.1	F3 — Shared identity: OIDC clients per app, OTP-verified account linking, multi-role, KYC reuse	Joint	26 Oct 26	13 Nov 26	15	3.4, 3.6
5.2	F4 — Push notifications (FCM/APNs) + role-scoped notification preferences	Srvin	26 Oct 26	13 Nov 26	15	3.4, D14
5.3	Hardening: regression, targeted pen test on identity, UAT; store submission	Joint	16 Nov 26	20 Nov 26	5	5.1, 5.2
5.4	◆ R2 LIVE — F3, F4	Joint	24 Nov 26	24 Nov 26	0	5.3
5.5	Hypercare + KT checklist sign-off (R2)	Srvin	24 Nov 26	30 Nov 26	5	5.4
6 Release R3 — F5 Cancellation & Refunds, F6 Web App (Players) (22 Dec 2026) (25 Nov 26 – 29 Dec 26)						
6.1	F5 — Cancellation & refunds for bookings and tournament registrations (gateway refund API, policy rules)	Srvin	25 Nov 26	11 Dec 26	13	5.4, D11
6.2	F6 — Web app for players: search, availability, booking, event registration, payments	Srvin	25 Nov 26	11 Dec 26	13	5.4, 3.6
6.3	Enabler — reconciliation & migration of existing duplicate accounts	Joint	25 Nov 26	11 Dec 26	13	5.4, D18
6.4	Hardening: regression, targeted pen test on refunds, UAT; store submission	Joint	14 Dec 26	18 Dec 26	5	6.1, 6.2, 6.3
6.5	◆ R3 LIVE — F5, F6	Joint	22 Dec 26	22 Dec 26	0	6.4
6.6	Hypercare + KT checklist sign-off (R3)	Srvin	22 Dec 26	29 Dec 26	6	6.5
7 Release R4 — F7 Generalised Partner Model, F8 Waitlist & Edit Alerts (27 Jan 2027) (23 Dec 26 – 02 Feb 27)						
7.1	F7 — Generalised partner/service model; coach, physio, nutritionist enabled by admin configuration	Srvin	23 Dec 26	15 Jan 27	18	6.5

WBS	Activity	Owner	Start	Finish	Days	Predecessors
7.2	F8 — Waitlist with time-boxed offers + event-edited-after-publish notifications	Srvin	23 Dec 26	15 Jan 27	18	6.5
7.3	Hardening: facility regression, UAT; store submission (reduced capacity over year-end)	Joint	18 Jan 27	22 Jan 27	5	7.1, 7.2
7.4	◆ R4 LIVE — F7, F8	Joint	27 Jan 27	27 Jan 27	0	7.3
7.5	Hypercare + KT checklist sign-off (R4)	Srvin	27 Jan 27	02 Feb 27	5	7.4
8 Release R5 — F9 Transaction Ledger, F10 Web App (Organisers & Partners) (23 Feb 2027) (28 Jan 27 – 02 Mar 27)						
8.1	F9 — Transaction Ledger: webhook ingestion + reconciliation, admin history/detail, PDF/CSV export, refund tracker	Srvin	28 Jan 27	12 Feb 27	12	7.4, D15
8.2	F10 — Web app for organisers & partners: events, tournaments, scoring, service & booking management	Srvin	28 Jan 27	12 Feb 27	12	7.4
8.3	Hardening: reconciliation check vs gateway, UAT; store submission	Joint	15 Feb 27	19 Feb 27	5	8.1, 8.2
8.4	◆ R5 LIVE — F9, F10	Joint	23 Feb 27	23 Feb 27	0	8.3
8.5	Hypercare + KT checklist sign-off (R5)	Srvin	23 Feb 27	02 Mar 27	6	8.4
9 Release R6 — F11 Split Settlement & Partner Payouts, F12 WhatsApp & Full Alert Catalog (23 Mar 2027) (24 Feb 27 – 09 Apr 27)						
9.1	F11 — Razorpay Route onboarding for all partner types + partner settlement view (web)	Srvin	24 Feb 27	12 Mar 27	13	8.4, D10
9.2	F12 — WhatsApp channel + full SOW Section 10.2 alert catalog	Srvin	24 Feb 27	12 Mar 27	13	8.4, D13
9.3	Enabler — offline import tools for completed-event data	Srvin	24 Feb 27	05 Mar 27	8	8.4, D19
9.4	Hardening: full end-to-end regression, performance test, full VAPT (pre-completion), UAT	Joint	15 Mar 27	19 Mar 27	5	9.1, 9.2, 9.3
9.5	◆ R6 LIVE — F11, F12 — PHASE 2A COMPLETE	Joint	23 Mar 27	23 Mar 27	0	9.4
9.6	Hypercare	Srvin	23 Mar 27	02 Apr 27	9	9.5
9.7	Infrastructure operations runbook & transition plan (SOW 15.1)	Srvin	08 Mar 27	26 Mar 27	15	9.1SS
9.8	Final KT: platform operations and architecture walkthrough	Srvin	24 Mar 27	02 Apr 27	8	9.5
9.9	◆ Phase 2A acceptance & KT checklist sign-off	SportSeek	02 Apr 27	02 Apr 27	0	9.7, 9.8
10 Continuous Support Obligations (20 Oct 26 – 21 Jun 27)						
10.1	Phase 1 production monitoring & bug fixes (SOW Section 16)	Srvin	20 Oct 26	09 Apr 27	124	2.16
10.2	90-day warranty per release (R1 → 18 Jan 2027 ... R6 → 21 Jun 2027)	Srvin	20 Oct 26	21 Jun 27	175	2.16

10. Dependency management

10.1 Dependency types

Type	Meaning	How it is managed
FS / SS	Finish-to-Start / Start-to-Start between activities	Tracked in the schedule; reviewed at every weekly demo
Feature → feature	A feature needs another feature live first (e.g. F9 Ledger needs F5 refunds)	Encoded in the release order (Section 10.2); the order is the plan's backbone
External (D-n)	Input or approval from SportSeek or a SportSeek-contracted third party	Dated register (10.3); escalated 5 working days before the need-by date; a late item moves its feature to the next train

10.2 Feature dependency chain

#	Upstream	Downstream	Why
I1	HLD & design system sign-off (23 Oct)	All features from R2	Specs and UI are the inputs the AI agents build from
I2	F3 Shared identity (R2)	F4, F6, F7, F9	Roles, login and per-person aggregation all hang off the shared identity
I3	F4 Push & preferences (R2)	F8 Waitlist & edit alerts, F12	Waitlist offers and edit alerts are notification-driven
I4	F5 Cancellation & refunds (R3)	F8 (booking states), F9 (refund tracker)	The Ledger reflects refunds; waitlist uses freed capacity
I5	F6 Web app — players (R3)	F10 Web app — organisers & partners	Shared web shell, auth and design components
I6	F7 Partner model (R4)	F10, F11	Partner web journeys and payouts need all partner types
I7	F9 Ledger (R5)	F11 settlement view	Settlements shown through the Ledger read model

10.3 External dependency register (SportSeek and third parties)

ID	Dependency	Owner	Need-by	Unblocks	Impact if late
D1	Mutual NDA and SOW/PO executed	SportSeek	29 Sept 26	1.1	Start of all work
D2	Phase 1 source code, DB schema, API docs; cloud, repo, store-console and gateway dashboard access	SportSeek	29 Sept 26	2.1, 3.1	Launch assessment cannot start
D3	Named Product Owner (decisions within 1 working day); UAT testers for the last week of every release	SportSeek	29 Sept 26	2.2, all UAT	Release slips to next train
D4	Launch scope and go-live criteria sign-off	SportSeek	01 Oct 26	2.2	Freeze date at risk
D5	Expected launch peak concurrent users (load-test target)	SportSeek	05 Oct 26	2.7	Load test runs against an assumed figure
D6	Legal content: privacy policy, terms, DPDP notice text, store listing copy & assets	SportSeek	09 Oct 26	2.8, 2.12	Store submission blocked

ID	Dependency	Owner	Need-by	Unblocks	Impact if late
D7	Apple App Store & Google Play developer accounts (SportSeek-owned) with release rights	SportSeek	29 Sept 26	2.12	Store submission blocked
D8	Requirement tool decision (JIRA or Trello) and workspace	SportSeek	02 Oct 26	3.2	Backlog managed off-tool temporarily
D9	Names of SportSeek developers joining the pod (2 recommended)	SportSeek	23 Oct 26	R2 onward	Capacity plan re-baselined
D10	Written confirmation that Razorpay Route (split settlement) is enabled for coach, physio and nutritionist partner categories	SportSeek / Razorpay	06 Nov 26	9.1	F11 moves to a later train; SOW 8.3 compliance design unconfirmed
D11	Refund & cancellation business policy (approver, timeframes, non-refundable items)	SportSeek	13 Nov 26	6.1	F5 moves to a later train
D12	Email/SMS templates for F1–F2 (SMS templates registered on DLT); full alert catalog and templates by 8 Jan 2027	SportSeek	05 Oct 26	2.9, 2.10, 9.2	F2 SMS reminders ship as email-only; F12 slips
D13	WhatsApp Business Solution Provider contract; Meta-approved message templates	SportSeek	05 Feb 27	9.2	WhatsApp part of F12 slips to next train
D14	Email provider account (by 5 Oct) and FCM/APNs credentials (by 30 Oct) in SportSeek accounts	SportSeek	05 Oct 26	2.9, 5.2	F1 or F4 slips
D15	Decision: Transaction Ledger in Admin + partner web only, or also in User/Partner apps (SOW 8.1 open item)	SportSeek	08 Jan 27	8.1	Ledger scope unconfirmed
D16	Warranty SLA numbers (acknowledge/resolve times) — SOW Section 16 open item	SportSeek	30 Oct 26	Support model	Default proposal applies
D17	UI/UX approvals turned around within 2 working days of submission	SportSeek	Rolling	3.6, 3.7	Feature rides the next train
D18	Approval of account-merge rules for existing duplicate identities	SportSeek	20 Nov 26	6.3	Identity migration moves to R4
D19	Historical completed-event data files for import	SportSeek	19 Feb 27	9.3	Import tool tested with synthetic data only
D20	Phase 2A NFR targets: API p95 latency, peak concurrency, uptime SLA	SportSeek	30 Oct 26	3.3, all hardening	Performance acceptance undefined
D21	Approval of Srivin's AI tooling on SportSeek code (enterprise terms, no training on client data, data-handling rules)	SportSeek	29 Sept 26	All	Delivery falls back to conventional pace and team size

11. Critical path and schedule risk



Each release builds on the one before: identity → refunds → partner model → ledger → payouts. External gates on the path: D21 AI approval (29 Sep), D11 refund policy (13 Nov), D18 merge rules (20 Nov), D10 Route confirmation (6 Nov), D13 WhatsApp templates (5 Feb).

Figure 4 — Phase 2A critical path

In a release train every release date is fixed, so the critical path is the **chain of feature dependencies**: identity (R2) → refunds and web shell (R3) → partner model (R4) → ledger and partner web (R5) → payouts (R6). A slip in an upstream feature pushes its dependants to a later train. The mitigation is to protect the upstream features first: identity gets the strongest engineers and the earliest spec.

11.1 Schedule risks

Risk	Likelihood / impact	Mitigation built into this plan
AI tooling not approved on day one (D21)	Low–Medium / High	Enterprise-terms tooling and a written AI usage policy offered at kick-off; data-handling rules agreed up front
Phase 1 assessment reveals more launch blockers than fit before 14 Oct	Medium / High	AI-assisted assessment in 3 days; Scope Gate 1 Oct; F1/F2 dropped before the launch is risked
F3 identity in a 3-week build window is tight	Medium / High	Spec and HLD start 5 Oct in parallel with launch; spikes in October; strongest pair on F3; linking rules decided at HLD
SportSeek decisions and approvals cannot keep pace with a monthly train	Medium / High	1-day decision / 2-day UI approval agreement (A4); weekly decision log; late items move to next train, not the whole release
Third-party approvals (Route, DLT, WhatsApp templates)	Medium / Medium	Dated in the register months ahead; F11/F12 sit in the last train to maximise lead time
AI-generated code quality or security regressions	Low–Medium / High	Human review of every merge, AI + SAST scans, full regression, targeted pen tests (Delivery Model §5, §14)
Year-end holidays reduce R4 capacity	High / Low	R4 build window extended to 3.5 weeks; holiday calendar agreed at kick-off

12. Milestones, gates and acceptance evidence

ID	Milestone / gate	Date	Decision owner	Acceptance evidence
1.2	Kick-off	29 Sep 2026	Joint	Governance charter, AI usage policy, access checklist
2.2	Launch Scope Gate	01 Oct 2026	SportSeek	Assessment report; frozen launch scope incl. F1/F2; go-live criteria
2.15	R1 Go/No-Go	19 Oct 2026	SportSeek	UAT sign-off; VAPT retest clean; load test; runbook; store status
2.16	R1 live — public launch	20 Oct 2026	Joint	Production smoke test; dashboards green
3.4 / 3.6	HLD and design-system sign-off	23 Oct 2026	SportSeek	HLD, ADRs, design system
4.4	M1 Foundation accepted	06 Nov 2026	SportSeek	IaC, CI/CD gates, observability
5.4	R2 live	24 Nov 2026	SportSeek	UAT sign-off; identity pen test clean
6.5	R3 live	22 Dec 2026	SportSeek	UAT sign-off; refund pen test clean; account reconciliation report
7.4	R4 live	27 Jan 2027	SportSeek	UAT sign-off; facility regression green
8.4	R5 live	23 Feb 2027	SportSeek	UAT sign-off; ledger reconciled to gateway
9.5	R6 live — Phase 2A complete	23 Mar 2027	SportSeek	UAT sign-off; full VAPT with no open critical/high
9.9	Phase 2A acceptance	02 Apr 2027	SportSeek	All SOW §13 deliverables; KT checklists signed

13. Anatomy of a monthly release

Every release R2–R6 follows the same four-week rhythm, so SportSeek’s team always knows what happens when.

Week	Build pod	SportSeek	Gate
Week 1	Plan from approved specs; AI agents generate implementation and tests; engineers review daily; next train's specs start	PO available for clarifications	Specs approved (DoR)
Week 2	Build continues; integration on Staging behind feature flags; weekly demo	Weekly demo feedback	—
Week 3	Feature complete (Friday); AI-generated regression and security scans; targeted pen test where applicable	UI approvals for next train	Feature complete
Week 4	Hardening; UAT support; store submission; runbook update	UAT (3 days); Go/No-Go (Mon of release week)	UAT sign-off; Go/No-Go
Release week	Release on Tuesday; one week of hypercare; KT checklist	KT checklist sign-off	KT signed

14. Resource plan: AI-native pod, loading and technical skills

A small, senior, AI-augmented pod replaces the four-squad team of the conventional plan. Every engineer is senior enough to judge AI output, because in this model review quality determines product quality. Loading is monthly average FTE; October includes mobilisation from 28 September. SportSeek developers (Section 14.5) are additional.

14.1 Technology stack and the skills it demands

Layer	Technology	Skills we staff for
Mobile apps	React Native (TypeScript), iOS and Android	OIDC/PKCE on mobile, push (FCM/APNs), deep links, schema-driven forms, store release engineering
Back end	.NET — ASP.NET Core, C#, EF Core with Npgsql	Modular monolith, OIDC identity, outbox messaging, Razorpay payments/refunds/Route, idempotent APIs
Database	PostgreSQL (schema per domain)	Expand/contract migrations, JSONB, exclusion constraints, geo search, identity de-duplication
Web	React + TypeScript, Next.js (proposed)	Server rendering for SEO, shared design tokens, data-heavy admin screens
AI engineering	AI coding agents (e.g. Claude Code) and AI assistants under enterprise terms	Spec writing, context engineering, agent guardrails, critical review of generated code and tests
Quality & operations	xUnit, Testcontainers, Jest, Detox/Maestro, Playwright, k6; IaC; OpenTelemetry	AI-generated test suites curated by engineers; CI/CD and observability

14.2 Pod composition and technical skills

Role	Seniority	Peak FTE	Person-months	Key technical skills	How AI is used in the role
Delivery Lead / TPM (AI-native delivery)	Senior (12+ yrs)	1	6.5	Release-train planning and dependency management; stakeholder and steering management; RAID and change control; metrics-driven delivery; governance of AI usage (policy, audit trail, data handling)	AI-generated status reports, RAID and dependency tracking from JIRA/Trello and repository data; JIRA / Trello
Solution Architect & AI Engineering Lead	Senior (12+ yrs)	1	6.25	ASP.NET Core modular monolith and domain design; PostgreSQL architecture; OAuth2/OIDC; event-driven integration; Razorpay incl. Route; React Native and React architecture; OWASP ASVS. Owns the AI engineering playbook: specs, prompt/context standards, agent guardrails and review rules	AI coding agents (e.g. Claude Code) for codebase analysis, spike prototypes and ADR drafting; C4 diagrams
Product Analyst (AI-assisted BA)	Mid–Senior (6+ yrs)	1	6.25	Story mapping; Given/When/Then acceptance criteria; booking, payments/refunds and partner domains; SOW traceability; UAT scenario design	AI drafts stories, acceptance criteria, edge cases and UAT scripts from the SOW and specs; analyst and PO refine
Product Designer (UX/UI)	Mid–Senior (6+ yrs)	1	4.75	Atomic design system; mobile and responsive web UI; usability testing; accessibility (WCAG 2.1 AA); design tokens shared by React Native and React	AI-assisted layout and copy exploration and design-to-code token export; Figma or agreed tool
Senior .NET Engineer (AI-augmented)	Senior (8+ yrs)	2	12.5	C# / ASP.NET Core; EF Core with Npgsql; OIDC implementation (e.g. OpenIddict); Razorpay payments, refunds, Route and webhooks; notification channel integrations; idempotent APIs; background processing	Spec-driven development with AI coding agents: agents generate code and tests from the approved spec, engineers review, harden and own every merge
.NET & PostgreSQL Engineer (AI-augmented)	Senior (8+ yrs)	1	6	Schema-per-domain design; EF Core migrations (expand/contract); JSONB with schema validation; exclusion constraints against double-booking; geospatial queries; query tuning; identity de-duplication and data-migration scripts; reconciliation SQL	AI-generated migration and reconciliation scripts, verified against Testcontainers PostgreSQL before any environment
Senior React Native Engineer (AI-augmented)	Senior (7+ yrs)	1	6.25	React Native + TypeScript on iOS/Android; OIDC with PKCE; push (FCM/APNs); deep links and app-switch handling; schema-driven forms; store release engineering with Fastlane; minimum-version enforcement	AI agents generate screens from design tokens and specs, and component and E2E tests; engineer reviews and tunes on real devices

Role	Seniority	Peak FTE	Person-months	Key technical skills	How AI is used in the role
Senior React / Next.js Engineer (AI-augmented)	Senior (7+ yrs)	1	4.5	React + TypeScript with Next.js; server rendering for SEO; shared design tokens; data-heavy admin screens (ledger tables, filters, exports); WCAG 2.1 AA	AI agents port Phase 1 mobile journeys to web against the shared API; parity checks generated from the mobile journey inventory
QA Automation Engineer (AI-assisted)	Mid–Senior (6+ yrs)	2	7.25	Test strategy and quality gates; API, mobile and web automation; payment/refund scenarios in Razorpay test mode; UAT support	AI generates API tests from OpenAPI specs, regression suites from user journeys, and test data; engineer curates and maintains the suite
DevOps / SRE Engineer	Senior (7+ yrs)	1	4.25	Infrastructure as code in SportSeek's cloud; CI/CD for .NET and React Native; managed PostgreSQL; OpenTelemetry observability; secrets; release automation; on-call	AI-assisted IaC authoring, pipeline configuration and log/incident triage
Security Engineer (VAPT, on demand)	Senior (8+ yrs)	0.5	1.75	Web, API and mobile penetration testing (OWASP WSTG, MASTG); targeted pen tests on identity (R2), refunds (R3) and payouts (R6); full VAPT before Phase 2A completion	AI-assisted SAST triage and threat-model drafting; manual testing by the specialist
Performance Engineer (on demand)	Mid–Senior (6+ yrs)	0.5	1	Load test design; .NET API profiling; PostgreSQL query analysis; capacity recommendations	AI-generated k6 scripts from the API catalogue; engineer designs workload models
Total			67.25		

14. Resource plan (continued)

14.3 Monthly resource loading (FTE)

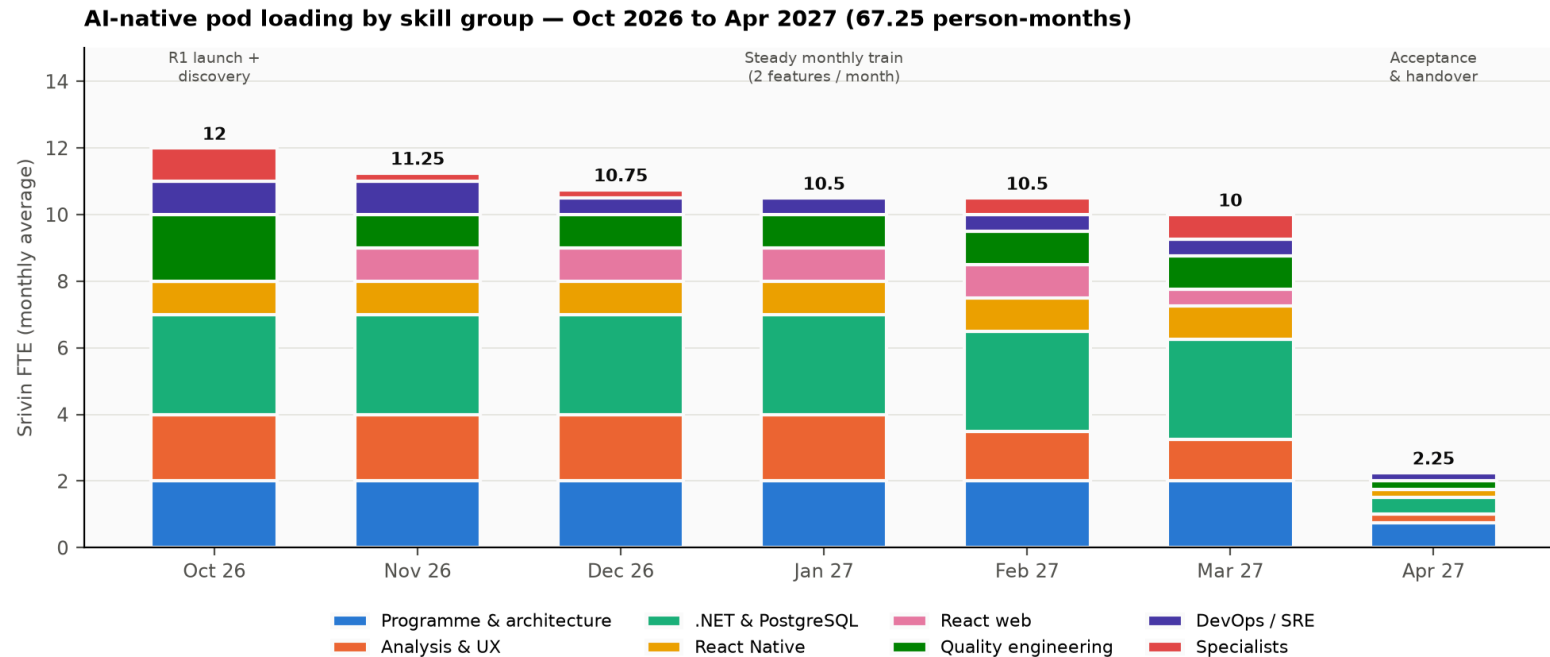


Figure 5 — AI-native pod loading by skill group

Role	Oct 26	Nov 26	Dec 26	Jan 27	Feb 27	Mar 27	Apr 27	Person-months
Delivery Lead / TPM (AI-native delivery)	1	1	1	1	1	1	0.5	6.5
Solution Architect & AI Engineering Lead	1	1	1	1	1	1	0.25	6.25
Product Analyst (AI-assisted BA)	1	1	1	1	1	1	0.25	6.25
Product Designer (UX/UI)	1	1	1	1	0.5	0.25	—	4.75
Senior .NET Engineer (AI-augmented)	2	2	2	2	2	2	0.5	12.5
.NET & PostgreSQL Engineer (AI-augmented)	1	1	1	1	1	1	—	6
Senior React Native Engineer (AI-augmented)	1	1	1	1	1	1	0.25	6.25

Role	Oct 26	Nov 26	Dec 26	Jan 27	Feb 27	Mar 27	Apr 27	Person-months
Senior React / Next.js Engineer (AI-augmented)	—	1	1	1	1	0.5	—	4.5
QA Automation Engineer (AI-assisted)	2	1	1	1	1	1	0.25	7.25
DevOps / SRE Engineer	1	1	0.5	0.5	0.5	0.5	0.25	4.25
Security Engineer (VAPT, on demand)	0.5	0.25	0.25	—	0.25	0.5	—	1.75
Performance Engineer (on demand)	0.5	—	—	—	0.25	0.25	—	1
Total Srivin FTE	12	11.25	10.75	10.5	10.5	10	2.25	67.25

How the loading follows the plan: October carries the launch (hardening, regression, VAPT, load test) alongside AI-assisted discovery, at 12 FTE. From November a steady pod of about 10–11 FTE runs the monthly train. Specialists (security, performance) join for the releases that need them. April is acceptance and handover only. SportSeek developers who have worked in the pod take over module ownership as Srivin rolls off.

14.4 Resource-to-WBS assignment matrix

● = primary responsibility; ○ = supporting or reviewing. Columns are the Level 1 WBS elements (Section 7.1).

Role	1 PM	2 R1 Launch	3 Design	4 Found.	5 R2	6 R3	7 R4	8 R5	9 R6	10 Support
Delivery Lead / TPM (AI-native delivery)	●	●	○	○	●	●	●	●	●	○
Solution Architect & AI Engineering Lead	○	●	●	●	●	●	●	●	●	○
Product Analyst (AI-assisted BA)		○	●		●	●	●	●	●	
Product Designer (UX/UI)			●		○	●	○	●	○	
Senior .NET Engineer (AI-augmented)		●	○	●	●	●	●	●	●	●
.NET & PostgreSQL Engineer (AI-augmented)		○	○	○	●	●	●	●	●	○
Senior React Native Engineer (AI-augmented)		●	○		●	○	●	○	○	●
Senior React / Next.js Engineer (AI-augmented)			○			●		●	●	
QA Automation Engineer (AI-assisted)		●	○	○	●	●	●	●	●	○
DevOps / SRE Engineer		●		●	○	○	○	○	●	●
Security Engineer (VAPT, on demand)		●			●	●			●	
Performance Engineer (on demand)		●						●	●	

14. Resource plan (continued)

14.5 SportSeek-provided resources

Role	Number	When	Responsibilities
Product Owner	1 (named)	Throughout; decisions within 1 working day	Backlog priority, spec approval, acceptance, SOW open items
Technical reviewer	1 (part-time)	HLD, ADRs, weekly demo	.NET / PostgreSQL / React Native review of designs
SportSeek developers	2 recommended (D9)	From R2 (26 Oct 2026)	Full pod members working with AI agents; become module owners after handover
UAT testers	2 recommended	Hardening week of every release; 15–19 Oct for R1	Business scenario testing across User, Partner, Admin and Web
Operations lead	1	From R3	Receives infrastructure handover (SOW §15.1)
Legal / compliance	As needed	By 9 Oct; per release as needed	Privacy, DPDP, refund policy, AI usage approval

14.6 Continuity and roll-off

- **Named, senior, stable pod:** the Delivery Lead, Architect, .NET, React Native and QA engineers stay for the whole engagement. Any change needs SportSeek notice and a two-week overlap.
- **Two-deep on critical skills:** .NET identity, PostgreSQL migrations, React Native releases and Razorpay integration are each held by at least two people across Srivin and SportSeek by R3.
- **Roll-off after sign-off:** engineers roll off only after the KT checklist for their features is signed. SportSeek keeps the AI-maintained documentation and the codebase assistant (Delivery Model §15).

15. Baseline control and re-planning rules

- **Baselines:** this plan is Baseline 0 (v2.0). **Baseline 1** is set at the R2 release review (24 Nov 2026), using measured AI-assisted velocity from the first build cycle.
- **Tolerances:** release dates do not move. If a feature is forecast to miss its train, the PO decides within 2 working days whether to move it to the next train or swap in a later feature of similar size.
- **Change:** new scope follows SOW §18 (written request → impact assessment in 5 business days → SportSeek approval) and is slotted into a future train.
- **Reporting:** weekly demo and status (features on track per train, dependency register, RAID), plus a monthly release review with the sponsor.

Appendix A. SOW-to-WBS traceability

SOW reference	Requirement	Feature / WBS
§3.1 Shared Identity; §7; §9.1 (M2)	Unified accounts, linking, roles, KYC reuse	F3 (5.1); 6.3
§3.1 Transaction Ledger; §8 (M3)	Ledger dashboard, statements, refunds, partner view	F9 (8.1); F11 (9.1)
§3.1 Booking/Events; §9.3 (M4)	Cancellation, waitlist, edit alerts, data model, import tools	F5 (6.1); F8 (7.2); 9.3; 2.5
§3.1 Partner & Service; §9.4 (M5)	Generalised service types; admin configuration	F7 (7.1); F11 (9.1)
§3.1 Notification; §10 (M6)	Push, WhatsApp, Email; alert catalog	F1, F2 (2.9–2.10); F4 (5.2); F12 (9.2)
§3.1 Web application	Web app for all existing functionality	F6 (6.2); F10 (8.2)
§6.2 NFRs	Security, performance, availability, DPDP, environments, observability	2.3, 2.6, 2.7, 4.x, all hardening WPs
§12.1 M1	Foundation	2.3, 4.1–4.4
§12.2 KT	KT after every milestone with checklist	KT per release (5.5, 6.6, 7.5, 8.5), 9.8
§13 Deliverables	Code, HLD/LLD, stories/tests, API docs, ERD, architecture, UI files, test suite, CI/CD, runbook, user docs, KT	3.x, 4.2, 9.7, all feature WPs
§14 Acceptance	Technical and functional acceptance	Hardening + Go/No-Go per release; 9.9
§15.1 Infra transition	Operate-then-handover	9.7
§16 Warranty & support	90-day warranty; Phase 1 support	10.1, 10.2
§18 Change management	Change process	1.5
